

Portland & Carver
Apartments

663 Portland Street

Excavation & Construction

Prepared by Geoff MacLean, P.Eng.

Job No. 38410

CONSTRUCTION MANAGEMENT PLAN

REVISION #	DATE	DESCRIPTION
1	JUL 26 2024	REVISED AS PER CLIENT COMMENTS
0	JUL 2024	ISSUED FOR PERMIT



36 Oland Crescent
Bayers Lake Business Park
Halifax, Nova Scotia B3S 1C6
www.sdmm.ca

t: 902-455-1537
f: 902-455-8479
c: 902-789-6374
e: gmaclean@sdmm.ca

Revision 1 – Sections; 1.1, 2.1, 2.2, 4.2, 5.1, 6, 7.2, 7.6, 8.1 & 8.3; Appendixes A, E, F, G & P.

Table of Contents

Section 1: Introduction	1
1.1: Project Description and Objectives	1
1.2: Project Contact Information	2
Section 2: Project Schedule and Logistics	2
2.1: Schedule	2
2.2: Key Dates	2
2.3: Hours of Work.....	3
Section 3 – Relevant Regulations & Guidelines	3
3.1: Occupational Health & Safety Regulations.....	3
3.2: Municipal Regulations & Guidelines.....	3
Section 4: Vehicle Management.....	4
4.1: Vehicular Traffic Control.....	4
4.2: Haul Route and Staging Areas	4
4.3: Vehicular Traffic Notifications	4
4.4: Emergency Vehicles.....	4
4.5: Parking	4
4.6: Bus Stops.....	4
4.7: Hazard Assessment.....	4
Section 5: Pedestrian Management	5
5.1: Pedestrian Protection	5
5.2: Pedestrian Safety.....	5
5.3: Pedestrian Traffic Notifications	5
5.4: Visually Impaired Persons.....	5
5.5: Accessibility	5
5.6: Hazard Assessment.....	5
5.7: Pedestrian Management Plans Rendering (PMPR) Signage.....	6
5.8: Pedestrian Detour Wayfinding Signage	6
Section 6: Encroachments & Disruptions	6
6.1: Demolition	6
6.2: Site Excavation.....	6

6.3: Site Services Connection.....	6
6.4: Construction Management Plan Element Inspection and Maintenance.....	7
6.5: Changes to the Construction Management Plan.....	7
Section 7: Environmental Factors.....	7
7.1: Damage to HRM Infrastructure	7
7.2: Protection of Trees	7
7.3: Line Painting and Temporary Crosswalks	7
7.4: Street and Right-of-Way Cleaning	8
7.5: Protection from Inclement Weather	8
7.6: Storm Water Management.....	8
7.7: Noise, Dust and Emission Control.....	8
7.8: Rodent Control	8
Section 8: Site Protection & Hoarding.....	9
8.1: Barriers & Fences.....	9
8.2: Snow removal	9
8.3: Gate Access and Egress.....	10
8.4: Hoarding Aesthetics.....	10
8.5: Sight Lines.....	10
8.6: Project Information and Contacts	10
Section 9: Lifting, Hoisting, and Crane Operations.....	10
9.1: Crane Use Overview	10
9.2: Transport Canada and Nav Canada Regulations.....	10
9.3: Aerodromes	10
Section 10: On-Site Safety and Security	11
10.1: Site Safety and Security Overview.....	11
10.2: Material Handling: Loading, Unloading, Delivery and Storage.....	11
10.3: Emergency Access & Egress.....	11
10.4: Security Site Lighting	11
10.5: Smoking Areas	11
10.6: Fire Suppression Systems	11
Section 11: Pre-Construction Consultation & Meeting	12
11.1: Pre-CMP Community Consultation.....	12

11.2: Project Information and Contacts 12

11.3: Preconstruction Meeting 12

11.4: Construction Notification 12

Section 12: Summary 12

Appendix A – Encroachment Plan A

Appendix B – Traffic Control Plans TCP B

Appendix C – Haul Route Plan C

Appendix D – Pedestrian Management Plan (PMP) D

Appendix E – Fence & Gates Information E

Appendix F – Hoarding Information F

Appendix G – Project Information Board G

Appendix H – Project Safety Signage H

Appendix I – Project Signage Specifications I

Appendix J – Sample Traffic Notification Letter J

Appendix K – Vehicular and Pedestrian Hazard Assessment K

Appendix L – Community Consultation Records L

Appendix M – HRM Tree Detail M

Appendix N – Rodent Control Plan N

Appendix O – CMP’s TCP & PMP Inspection Records O

Appendix P – Concrete Delivery Schematic P



Prepared by

G.K. MacLean, P. Eng.

In consultation with the construction manager, traffic control company and HRM

Section 1: Introduction

1.1: Project Description and Objectives

The owner/developer is planning to construct an apartment building on their land located at 663 Portland Street in Dartmouth, Nova Scotia. In preparation for this development the existing wooded lot will be cleared and excavated to make way for the new building. The planned development will include 81 residential units and main floor commercial space within a 6-storey building accessed from Portland Street. This CMP has been prepared to address excavation, services and building construction.

Where the development is planned to be 2m (6.5ft) from the street line with 2 level of underground parking, deep excavations of +/- 5.12m (15ft) below grade are anticipated fronting the HRM Right of Way (ROW) along Portland Street. Given the building is setback +33m (108ft) from the street line along Carver Street and +12.5m (41ft) from the Portland Street sidewalk; a sidewalk encroachment is not anticipated for this project. However, to provide room for ground sloping during excavation, we are proposing a minimal ROW encroachment occupying space behind the sidewalk of Portland Street. For public safety from excavation limits and construction activities the project is planned in two phases. Phase one, construction fencing will be installed along the street line and around the perimeter of the site, prior to excavation. Phase two, a portion of the HRM ROW will be hoarded off extending construction fencing 4.6m (15ft) from the street line with a row of interlocking F-type concrete barriers installed in front along Portland Street. All concrete operations and material deliveries will be staged within private property during construction with the main access gate stationed off Carver Street and a secondary gate off Portland Street. Throughout construction two-way vehicular traffic and pedestrian traffic will be maintained along both streets.

The developer's contractor will coordinate driveway access interruptions with the neighbours (16 & 17 Carver Street) during water service installation within the ROW.

Only during service work and driveway installations do we anticipate short term temporary lane drops on Portland Street and Carver Street.

The project borders residential properties along its northern, western property lines, a residential property and vacant HRM land along its eastern property line and across Portland to the south is a commercial property the houses Shoppers Drug Mart. All neighbouring properties will remain undisturbed throughout the project.

This CMP document is intended to be an evolving document to help guide the project team to mitigate impacts to the adjacent community before they arise and to address unforeseen issues. SDMM, together with the Developer, contractor, and traffic control company, have prepared this Construction Management Plan (CMP) following HRM's CMP (2020) guidelines and administrative order (2018-005-ADM) in an effort to reduce potential negative impacts on the surrounding community, due to construction activities for this project.

The most up-to-date version of this document will be kept on-site at all times during construction. Should ownership or contracting services change throughout the course of this project, HRM will be notified immediately, and new parties will be required to comply with the approved CMP in writing.

1.2: Project Contact Information

The project team for the proposed development consists of:

Role	Name	Contact	Address	Phone
Owner/Developer	3338408 Nova Scotia Limited	Johnny Anjoul	11 Kelvin Grove Halifax, NS, B3V 1G3	(902) 209-6902 24 Hour Emergency Contact
Site Contractor	Atlantic Road Construction and Paving	Greg MacDonald	6 Belmont Avenue, P.O. Box 89 Eastern Passage, NS B3G 1M7	(902) 830-6411
Traffic Control Company	Frontline Traffic Services	Tyler Hayman	6 Belmont Avenue, P.O. Box 89 Eastern Passage, NS B3G 1M7	(902) 818-5548
Rodent Control Company	Rentokil Pest Control		51 Duke Street, Bedford, NS B4A2Z2	(902) 835-2304

Section 2: Project Schedule and Logistics

The following is a brief summary of anticipated major project milestones broken down by phase:

2.1: Schedule

Project Phase	Start Date		End Date	Time Period
Rodent Control Program	Jul 15, 2024	-	Dec 15, 2024	5 months
Site Excavation	Aug 1, 2024	-	Nov 30, 2024	4 months
Substructure	Dec 1, 2024	-	Feb 28, 2025	3 months
Superstructure	Jan 1, 2025	-	Jan 31, 2026	12 months
Building Construction	Jan 1, 2024	-	Jan 31, 2026	12 months
Service Abandonments	n/a	-	n/a	-
Service installs (within ROW)	Sep 7, 2024	-	Sep 15, 2024	2 weekends
Service installs (site)	Mar 1, 2025	-	April 30, 2025	2 months
HRM Right of Way Flat Works	Aug 1, 2025	-	Aug 30, 2025	1 month
Site Flat Works	Sep 1, 2025	-	Oct 30, 2025	2 months

2.2: Key Dates

- Setup safety fencing along property lines August 1, 2024
- Install encroachment February 1, 2025
- Finish encroachment January 31, 2026
- Duration of encroachment 12 months
- Temporary sidewalk encroachments and/or temporary travel lane closures:
 - Carver Street water service install September 7 – 8, 2024
 - Portland Street sewer service install (off Street within ROW) September 14 – 15, 2024
 - For site access driveway installation (Portland Street) September 16-17, 2024
 - For final driveway installation (Portland Street) August 4-8, 2025
 - For final driveway installation (Carver Street) August 11-15, 2025

The encroachment areas are shown in the appendix for reference.

2.3: Hours of Work

Work will generally take place during normal working hours as outlined in HRM’s Noise By-Law and Traffic Control Manual Supplement; these are noted below.

- Monday to Friday: 7:00 a.m. – 9:30 p.m.
- Saturdays: 8:00 a.m. – 7:00 p.m.
- Sundays & Statutory Holidays: 9:00 a.m. – 7:00 p.m.
- Servicing Work: Noted Above

Although work is not expected to be required outside of the times listed above, if, for any reason, work is anticipated to be required outside of these hours, the contractor will apply to HRM for approval 5 business days (minimum) in advance of such work and obtain approval prior to proceeding. It is noted that HRM’s Noise By-Law cannot be altered without HRM council approval; work must adhere to the Noise By-Law. Note that construction noise exemptions may be granted where construction noise is planned to take place during prohibited hours of the N-200 By-law. The landowner to apply for this separately under the Construction Noise Exemption process.

Section 3 – Relevant Regulations & Guidelines

3.1: Occupational Health & Safety Regulations

This CMP shall be utilized in agreement with all applicable Provincial and Federal Occupational Health and Safety Regulations. At a minimum, construction activities must at all times meet the standards of:

- a) National Building Code of Canada, as adopted and modified under the Building Code Act and the Nova Scotia Building Code Regulations made under that Act;
- b) Nova Scotia Occupational Health and Safety Act, and the Nova Scotia Occupational Safety General Regulations made under that Act;
- c) The Transportation Association of Canada (TAC)’s Manual of Uniform Traffic Control Devices for Canada (MUTCDC); and
- d) Nova Scotia Temporary Workplace Traffic Control Manual (NSTCM).

3.2: Municipal Regulations & Guidelines

In addition to the Provincial and Federal standards referenced in Section 3.1, this CMP shall be utilized in agreement with and meet, at a minimum, the standards of all relevant municipal by-laws including, but not limited to, the following:

- a) HRM Design Guidelines;
- b) HRM Standard Details;
- c) S-300 Streets;
- d) E-200 Encroachments;
- e) B-201 Building;
- f) N-200 Noise;
- g) T-600 Trees;
- h) S-900 Controlled Access Streets;
- i) T-400 Truck Routes;
- j) W-101 Discharge into Public Sewers;
- k) B-600 Blasting;
- l) HRM TCM Supplement;
- m) G-200 Grade Alteration and Stormwater management;
- n) Admin Order 2018-005-ADM regarding encroachments; and
- o) Admin Order 2020-010-OP regarding stormwater management standards for development activities.

Section 4: Vehicle Management

Prior to any construction activity, all temporary workplace traffic control devices and signage will be in place as per the Nova Scotia Temporary Workplace Traffic Control Manual (latest edition). The traffic control company will install the signage and ensure that they are maintained throughout the project. This project's Traffic Control Plans (TCPs) are listed in the Appendix.

4.1: Vehicular Traffic Control

A series of Traffic Control Plans (TCP) has been prepared by the traffic control company and is provided in the Appendix.

Throughout all phases of construction two-way vehicular traffic will be maintained along the Portland Street and Carver Street. Only during service work and driveway installation do we anticipate short term temporary lane closures being required. Please refer to the appendices for required encroachment plan and traffic control plans.

4.2: Haul Route and Staging Areas

The truck Haul Route Plan has been prepared by the traffic control company and is provided in the appendix.

The selected route is intended to minimize traffic congestion and maximize pedestrian safety. During all construction phases vehicles will enter and exit the site at the gate location(s) which will be clearly marked. Throughout all phases of construction, concrete and material deliveries shall be contained within private property and the encroachment.

4.3: Vehicular Traffic Notifications

Should any traffic disruptions be required, notifications will be distributed to properties in the impacted area a minimum of five (5) days in advance of vehicular traffic closures. Refer to sample notification letter in the appendix.

4.4: Emergency Vehicles

In the event of unforeseen emergency situations, the site will remain accessible to emergency vehicles at all times.

4.5: Parking

Un-metered on street parking will be closed along Carver Street directly adjacent of both sides of the existing driveway that accesses the project site to allow room for construction vehicle access. On street parking will be affected by this project. It is noted that passenger vehicles are not permitted to park within any encroachment areas. To minimize parking requirements in adjacent neighbourhoods, site workers will utilize private property and workers will be encouraged to carpool or rely on public transit.

4.6: Bus Stops

There is a bus stop in the vicinity of the project site adjacent to civic 669 Portland Street directly in front of vacant HRM land and on the opposite side of the Portland Street of the project fronting civic 660. Bus service travelling along Portland Street should not be affected by this project.

4.7: Hazard Assessment

A vehicular and pedestrian hazard assessment is provided in the appendix. Any additional site hazards identified or encountered after work has commenced will be added to this list. All personnel on-site will be required to review this list and encouraged to identify additional potential hazards and hazard mitigation methods.

Section 5: Pedestrian Management

A Pedestrian Management Plan (PMP) has been prepared by the traffic control company and is provided in the appendix.

Throughout construction the sidewalk will remain open to pedestrians on both streets. Only during service and driveway reinstatement will the sidewalk be temporarily closed. Pedestrian traffic will be maintained with use the existing crosswalks at the intersections of Carver Street and Jersey Drive along Portland and on the opposite side of the street along Carver with the aid of traffic control.

5.1: Pedestrian Protection

Pedestrians will be protected by physically distancing them from the project. A combination of rigid fencing and F-type concrete jersey barriers will delineate the project during the construction activities. Rigid fencing will be covered with opaque covering and will extend a minimum 3m from the public right-of-way, to block view of the site. Refer to the appendix for examples of the barriers and fencing.

5.2: Pedestrian Safety

Pedestrian safety will be maintained by implementing appropriate signage as shown on the PMP. All navigation and safety signage indicating alternative sidewalks and potential hazards will be inspected and maintained regularly.

5.3: Pedestrian Traffic Notifications

Notifications will be distributed to properties in the impacted area a minimum of five (5) days in advance of pedestrian traffic impacts. A sample traffic notification letter can be found in the appendix. HRM must be notified prior to issuing the notification to neighbours.

5.4: Visually Impaired Persons

In keeping with CNIB requirements and as outlined on their 'Clearing Our Path' website; various items will be incorporated into the pedestrian management signage and barriers. Such as, high visibility contrasting colours with appropriate font types (mix of upper and lower-case lettering), font sizes (between 16mm to 51mm) and sign colours (orange background with black lettering or white background with black lettering).

The contractor will use bright orange sawhorse barricades complete with bold-font signage to identify sidewalk termination points. Sawhorse barriers will incorporate lower cross members, painted and marked consistent with the rest of the sawhorse, these added cross members will be placed near the ground to aid visually impaired persons using a cane. Reflective tape will also be placed on the ends of fencing, hoarding, sawhorse barricades, and concrete barriers to help delineate pedestrian routes and disruptions. Signage and tape colours will vary but will comply with the colour/brightness contrast as outlined by the CNIB website; examples are black/white, orange/black or dark red/white combinations.

5.5: Accessibility

High visibility signage will be used to assist pedestrians to easily navigate around all project related blocked sidewalks.

5.6: Hazard Assessment

A vehicular and pedestrian hazard assessment is provided in the appendix. Any additional site hazards identified or encountered after work has commenced will be added to this list. All personnel on-site will be required to review this list and encouraged to identify additional potential hazards and hazard mitigation methods.

5.7: Pedestrian Management Plans Rendering (PMPR) Signage

The need for a rendered map displayed for pedestrians showing the detoured pedestrian routes are not anticipated for this project.

5.8: Pedestrian Detour Wayfinding Signage

The need for pedestrian wayfinding signage directing pedestrians to adjacent businesses is not anticipated for this project.

Section 6: Encroachments & Disruptions

A sidewalk encroachment is not anticipated for this project. Only during service work and driveway installation will pedestrian & vehicle traffic be affected as temporary lane closures will be required. This will temporarily close parking along Carver Street on either side of the existing driveway that accesses the project site and direct pedestrians to the opposite side of street with use of existing crosswalks at Portland and traffic control on Carver. To keep the public away from potential hazards a combination of construction fencing with opaque covering and F-type concrete barriers will delineate the project site and encroachment. All fencing must be anchored to the ground to prevent unintentional movement or overturning due to snow and wind loads.

Throughout the project, fencing will be positioned to not obstruct vehicle sight lines. In areas adjacent to the site gates open mesh rigid fence behind of the site barriers to not obstruct sight lines.

Should any utility or traffic disruptions be required, the contractor will first apply to HRM for approval, a minimum of five (5) business days in advance of such work and will then notify neighbours of these disruptions in a timely fashion.

6.1: Demolition

Demolition is not required for this project.

6.2: Site Excavation

This includes deep excavation and removal of common site material. The development is planned to have 2 levels below street grade fronting Portland Street. If bedrock is found, the contractor will need to apply for a blasting permit and adhere to the HRM blasting by-law and conditions of the blasting permit. Alternatively, if a blasting permit can not be obtained the site's bedrock will be broken by a series of rock breakers to reach footing elevation. If soft soils are found, temporary shoring may need to be utilized to retain ground elevations.

6.3: Site Services Connection

This includes installation of new water and sewer service lateral to their respective mains. The water service work is anticipated to require a lane drops with temporary workplace signage incorporated (refer to the Service Installation Traffic Control Plans (TCP) in the appendix). HRM requires that this service work be limited to weekends only to minimize traffic disruptions. The target dates for this work are provided in the "Key Dates" section above with time of installations adhering to the Noise By-Laws noted above. The intent will be to complete this servicing work and reinstate the street as quickly as possible in order to minimize disruptions to the public.

Before scheduling site services connections, the contractor will notify all neighbouring properties, of the intended timeline for this work. A sample notification letter is included in the appendix.

The contractor intends to reinstate the street cut during the season of work. It is noted that street cuts cannot be left gravel or open. HRM reinstatement specifications must be met, and the travel way must be hard surfaced prior to

reopening to the public. Asphalt, concrete curb and sidewalk reinstatement must be completed within 72 hours of disturbance and will be considered temporary if reinstated after October 31st or prior to May 1 in which case permanent reinstatement will be completed by June 15.

6.4: Construction Management Plan Element Inspection and Maintenance

Construction management plan elements will be inspected daily to ensure continued adherence to this CMP. Any deficiencies identified will be reinstated immediately. A CMP's TCP & PMP inspection report summary will be completed for the project, including information on what maintenance activities were conducted. This report must be kept on site at all times and be available to HRM upon request.

6.5: Changes to the Construction Management Plan

All departures from the CMP regardless of the significance must be submitted to the Municipality 10 days in advance for review and approval. Any required changes or modifications to the approved CMP will be submitted to HRM for review and approval prior to implementation.

Section 7: Environmental Factors

7.1: Damage to HRM Infrastructure

Existing HRM infrastructure damaged during construction adjacent to the project will be reinstated and be completely replaced. This includes reinstatement of the HRM lawn, HRM sidewalk, and curb and gutter post construction. It is anticipated that HRM infrastructure across the street will not be impacted by excavation or other construction activities. However, while efforts will be made to avoid damage, it is anticipated that additional portions of existing curbs, gutters and HRM lawn may become damaged during the construction process which would require repairs or replacement. Pending HRM's review prior to and after construction and subject to damage due to construction activities, the landowner acknowledges that items may require to be fully replaced rather than repaired. The landowner also acknowledges that any costs incurred to repair or replace this public infrastructure are the responsibility of the owner.

For reinstatement timeline requirements, it is noted that asphalt and concrete curb reinstatement must be completed within 72 hours of disturbance and will be considered temporary if reinstated after October 31st or prior to May 1 in which case permanent reinstatement will be completed by June 15 of the following construction season.

7.2: Protection of Trees

There is a seventeen (17) HRM owned street trees within the public right-of-way directly adjacent to the project site on Portland Street. It is noted that HRM street trees shall not be touched prior to approval and/or compensation agreements between the landowner and HRM Urban Forestry are in place. Adjacent street trees are to be protected during construction in accordance with the HRM Tree Bylaw (T-600). Refer to HRM tree protection detail in the appendix.

Due to the excavation limits, planned driveway, sewer service work, walkway location and retaining wall placement at Portland Street, we are proposing to remove sixteen (16) HRM owned street trees within the public right-of-way directly in front of the project on Portland Street in coordination with HRM. Sizes and locations are shown on the encroachment plan.

7.3: Line Painting and Temporary Crosswalks

Temporary line painting such as altered centreline or temporary crosswalk are not anticipated for this project.

7.4: Street and Right-of-Way Cleaning

The portion of public street adjacent to the project will be cleaned daily of any debris from trucks and silt, dirt, or rock that migrates beyond the encroachments. A sweeper truck will be utilized as required. Rock pads will be installed and maintained at all site entrances behind the curb line to knock dirt free from truck tires with aim to reduce off tracking of site soils.

7.5: Protection from Inclement Weather

To protect the public from construction debris during inclement weather, the project site will be enclosed by fencing complete with dust control covering, the site will be regularly reviewed and cleaned, with loose items secured when not in use.

7.6: Storm Water Management

During construction, nearby catch basins may be fitted with silt bags and/or filter fabric to prevent debris from entering the storm system and maintained until final reinstatement is complete. Stormwater collected inside the project site will be directed to temporary stormwater settling ponds situated within the building footprint to allow clean water to be pumped into the existing public sewer systems. Excavation dewatering to municipal systems require a permit to be obtained from Halifax Water via p2@halifax.ca, and must follow the strict adherence to Halifax Water regulations. The contractor must prevent erosion or siltation of surface runoff from leaving the construction site through the use of erosion and sedimentation controls (See NSECC Erosion and sedimentation control handbook for construction sites). Sediment ponds may be shifted and positioned as desired by the site contractor during mass excavation however will generally be placed in localized low points within the building excavation.

7.7: Noise, Dust and Emission Control

The contractor will at all times adhere to the HRM Noise Bylaw (N-200) unless approved under HRM exemption process. No work will take place on the project site outside those hours identified in section 2 of this report, unless HRM grants an exception.

Dust mitigation for this project will be achieved using rock pads for trucks exiting the site. A water truck and sweeper truck will also be utilized to help prevent dust from becoming airborne and, when required, calcium may need to be used to mitigate dust migration. Additionally, mesh on the inside of the fencing will help to contain any airborne dust inside the site.

Breaking of rock may occur and rock faces cleared to form a wall. Mesh will be used on the inside of all construction fencing to mitigate dust control.

All construction vehicles will be required to use the loading area for parking and idling to keep exhaust emissions within the construction zone. Vehicles will be staged so that idling will not occur for more than 3 minutes at a time.

As indicated above, all work shall be completed in accordance with the HRM Noise By-Law.

7.8: Rodent Control

Rodent movement increases during construction activities. The owner has engaged a rodent control company, to utilize the established Rodent Control Plan (RCP) to help mitigate rodent movement prior to and during site excavation and building construction. The RCP applies to all project phases with the goal of preventing movement of rodents off-site. The RCP will consist of a baiting and monitoring program. Bait stations (traps) will be placed as outlined in the NPMA Pest Management Standards for Food Processing & Handling Facilities.

The RCP was engaged two weeks prior to the commencement of site excavation to help to lower the number of active rodents in the project area. Bait stations positioned along existing buildings and fence lines prior to excavation. Bait stations positioned along the edges of the project and secured in place using wooden stakes (for open sodded and dirt locations), weighted patio stones (behind walls and on paved areas), and zip-ties (fixed to fences) as per typical industry standards.

Refer to the appendix for a copy of the Rodent Control Plan.

Section 8: Site Protection & Hoarding

8.1: Barriers & Fences

The project will be delineated with a mix depending on the phase. A combination of weighted down modular construction fencing and F-type concrete jersey barriers, total height shall be 1.8m or 6ft as per the noted administrative order. This fencing will be covered with an opaque dust control mesh of high quality which will extend a minimum 3m from the public right-of-way. This screening is described in the appendix and will block passersby or tourists view of the construction site. All fencing will have dust control mesh and must be anchored down to prevent unintentional movement or overturning due to snow or wind loads. In addition, the adjacent HRM street trees in front of the project on Portland Street will be protected as per HRM's tree protection details with orange snow fencing delineating the existing tree lawn between the sidewalk and street curb

Throughout the project, fencing will be situated to not obstruct vehicle sight lines.

Along the private sidelines where non-vehicular traffic is present, the hoarding will be delineated by weighted modular 1.8m (6ft) high fencing or existing fencing where it is at least 1.8m tall.

The F-type barriers and fencing that define the encroachment will adhere to the Encroachment Plan which is to scale includes dimensions and can be found in the appendix. These areas can be measured for the administering of applicable fees. Encroachment areas and fees will be based on the areas within the public right-of-way enclosed by the barriers and fencing.

Installation of F-Type concrete barriers, fencing and covering will take place during regular working hours as noted above. This work will be scheduled by the contractor after the HRM's pre-construction meeting has been held. HRM will coordinate this pre-construction meeting; the landowner, contractor and traffic control company will attend this site meeting. During the process of erecting and tearing down the traffic barriers, fencing and opaque covering defining the encroachment, traffic control elements will be implemented as per the Traffic Control Plan(s) in the appendix. All work and any traffic interruptions will be coordinated by the contractor who will notify HRM a minimum of 5 business days before work is scheduled to begin.

It is noted that surplus fencing must be stored and installed from private property when relocated for deliveries and be routinely re-established to keep the site secure. Surplus fencing cannot be stored within HRM's right-of-way.

8.2: Snow removal

The landowner will be responsible to remove snow and ice as required to ensure that emergency access is maintain to the project site, this includes fire hydrants. The contractor will not dump snow or ice onto adjacent property and will truck snow off site as required to prevent the unsafe build-up of snow piles.

8.3: Gate Access and Egress

The site will be accessible through gates. These gates are the only locations that will receive equipment/materials during construction, gates will remain closed and will be locked at all times after work hours. In cases of emergencies, on-site workers will exit the project site through these gates. These gates will remain unlocked at all times when workers are on site in case of emergency allowing unrestricted emergency response units access to the site.

Construction access gates are planned to be stationed along the property line at the proposed driveways on both streets during phase one with one gate relocated along the Portland Street encroachment in phase two. The gate stationed off Carver Street will be use as the main access gate during construction activities to facilitate deliveries. Gates are to swing into site, remain closed when not in use and locked after hours.

Any existing fire hydrants located adjacent to the site will remain protected from construction activities. These fire hydrants, along with the existing department connections will be accessible to firefighters throughout all phases of the project. Adjacent existing hydrants and fire department connections are not anticipated to be affected by construction.

8.4: Hoarding Aesthetics

The site hoarding will resemble that shown in the appendix; encroachment fee reductions are not anticipated.

8.5: Sight Lines

Rigid fencing and signage will be installed as per the CMP drawings such that vehicle sight lines are maintained around corners, particularly at driveway access points and existing intersections.

8.6: Project Information and Contacts

To encourage communication between the project team and the public, contact information will be provided on Project Information Boards; these will be posted prominently around the project site on the fencing; refer to the appendix for a copy of the Project Information Board and the Encroachment Plan for the planned locations. Refer to the signage specification within the appendix describing the required size, materials, mounting hardware, etc. of these signs.

Section 9: Lifting, Hoisting, and Crane Operations

9.1: Crane Use Overview

A tower crane is not anticipated for this project. Zoom boom, telehandlers, boom trucks and/or small mobile crane trucks will be brought to site to accommodate lifting and hosting materials to upper levels. Concrete placement will be facilitated by a concrete pump trailer and delivery trucks stationed within owner's private property (see concrete delivery schematic within the appendix). Material delivery trucks will be stationed within owners' private property and will be operated under the direct supervision of a licensed crane operator.

If lifting operations are required over the public realm, this area will be closed to access. In all cases of lifting, extreme care will be used to ensure public and worker safety.

9.2: Transport Canada and Nav Canada Regulations

We do not anticipate the use of a tower crane for this project.

9.3: Aerodromes

We do not anticipate the use of a tower crane for this project.

Section 10: On-Site Safety and Security

10.1: Site Safety and Security Overview

The contractor will adhere to all Occupational Health & Safety requirements throughout the completion of this project. At a minimum, the following safety protocols will be utilized to further enhance site safety and security:

- a) All workers will be required to have proof of up-to-date safety training;
- a) Personal protective equipment (PPE) will be required for all personnel on site;
- b) Adequate signage will be placed outside the hoarding, which will warn of hazards that may exist;
- c) Gates will be locked and the perimeter fencing secured to provide security against public access during off work hours and will be monitored during operation;
- d) Hoarding will clearly state “No Trespassing – Construction Personnel Only” & PPE requirements will be clearly identified (e.g., “Hard Hats and Safety Footwear Must Be Worn Beyond This Point”);
- e) Regular safety inspections will be conducted to ensure suitability of hoarding and other safety devices;
- f) Emergency contact information to be prominently posted as per the Project Information Board.

10.2: Material Handling: Loading, Unloading, Delivery and Storage

The contractor will adhere to the procedures stipulated in the Haul Route Plan for delivery of materials. Delivery vehicles will use the designated gates for entry and exit. Timing of deliveries will be coordinated to have the least possible negative impact on regular traffic. The staging and delivery area will be coordinated by the delivery companies and site personnel, trucks will be housed within private property accessed from Carver Street.

10.3: Emergency Access & Egress

The site will be accessible through gates to facilitate construction vehicle access. In cases of emergencies, on-site workers will exit the project site through these gates. These gates will remain closed but unlocked at all times when workers are on site in case of emergency allowing unrestricted emergency response units access to the site. Gates will be locked and secured afterhours to provide security against public access during off work hour. Emergency contact information will be posted on project information boards surrounding the site, refer to the CMP plan for details.

Gates are to remain closed at all times unless being used for deliveries to maintain a controlled access site preventing access by the general public to the construction site.

10.4: Security Site Lighting

Security site lighting is not anticipated for this project.

10.5: Smoking Areas

On site smoking areas will not be provided as this will be a smoke-free site.

10.6: Fire Suppression Systems

There is one (2) existing fire hydrants along Carver Street in vicinity of the project, one (1) in front of civic 11 and one (1) near the corner at civic 651 Portland Street. Any existing fire department connections (FDC) adjacent to the site will remain outside the project area and distanced from construction activities. Fire hydrants, along with any existing FDCs will be accessible to firefighters throughout all phases of the project.

There are no proposed fire department connections as part of this project.

Section 11: Pre-Construction Consultation & Meeting

11.1: Pre-CMP Community Consultation

Due to the current pandemic, the landowner will forego the community consultation meeting. A construction notification letter will be delivered to the properties neighbouring the construction site as well as HRM staff, notifying them of the expected work with contact information for questions and feedback. As part of this notification the surrounding community and businesses will be offered to sign up for a monthly construction project notification from the development. It is understood, HRM requires a confirmation letter from the applicant confirming delivery of notification letters to affected residents. A map indicating these properties has been included in the appendix.

11.2: Project Information and Contacts

To encourage communication between the project team and the public, contact information will be provided on Project Information Boards; these will be posted prominently around the project site on the fencing; refer to the appendix for a copy of the Project Information Board and the CMP Plan for the planned locations. Information on signage size and materials is outlined in the appendix.

11.3: Preconstruction Meeting

Prior to construction the landowner, contractor and traffic control company will attend a pre-construction meeting with HRM staff to review the CMP document on site. HRM's engineering technician will confirm the date and time of this meeting; and may wish to waive the requirement.

11.4: Construction Notification

Approximately five (5) business days prior to the encroachment, an additional notification will be circulated to the neighbouring properties, notifying them that work is starting on site.

Section 12: Summary

This construction management plan was prepared with the goal to minimize negative impacts to the community, pedestrians, and traffic throughout the scope of this project. This plan will be used as a minimum standard and any further safety protection required or methods to provide a more positive environment will be used throughout construction work as necessary.

Should you have any questions or comments related to this document, please contact SDMM. For all construction-related inquiries, please contact the landowner, contractor, or traffic control service provider.

Regards,



Servant, Dunbrack, McKenzie & MacDonald Ltd.

Geoff MacLean, P.Eng.
Project Engineer

Z:\SDMM\38000-38999\38400\38410\CMP\Rev1\663 Portland Street - CMP (Rev1) - 38410.docx

APPENDIX

Appendix A – Encroachment Plan

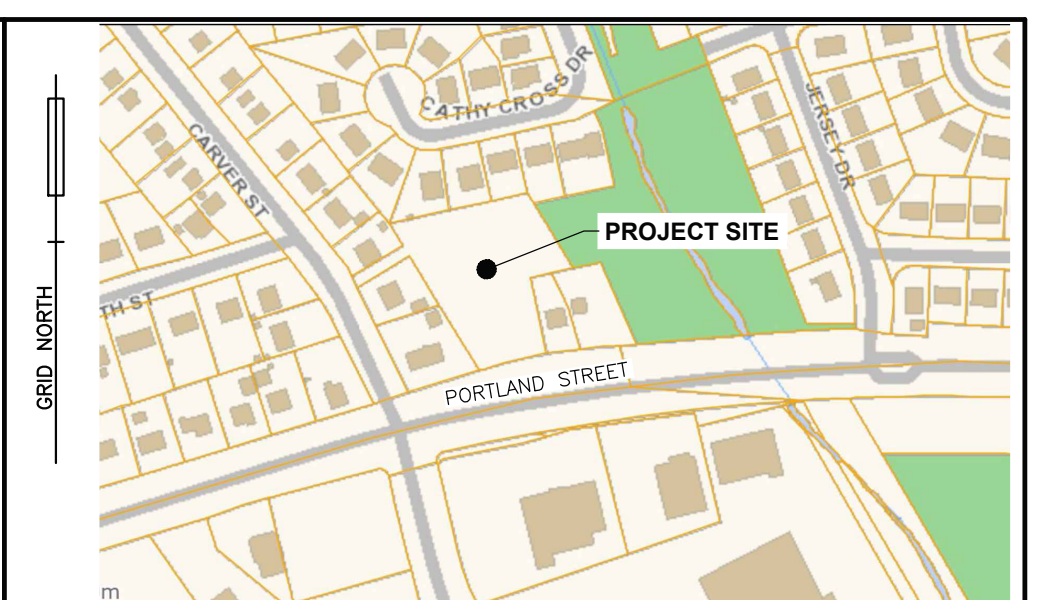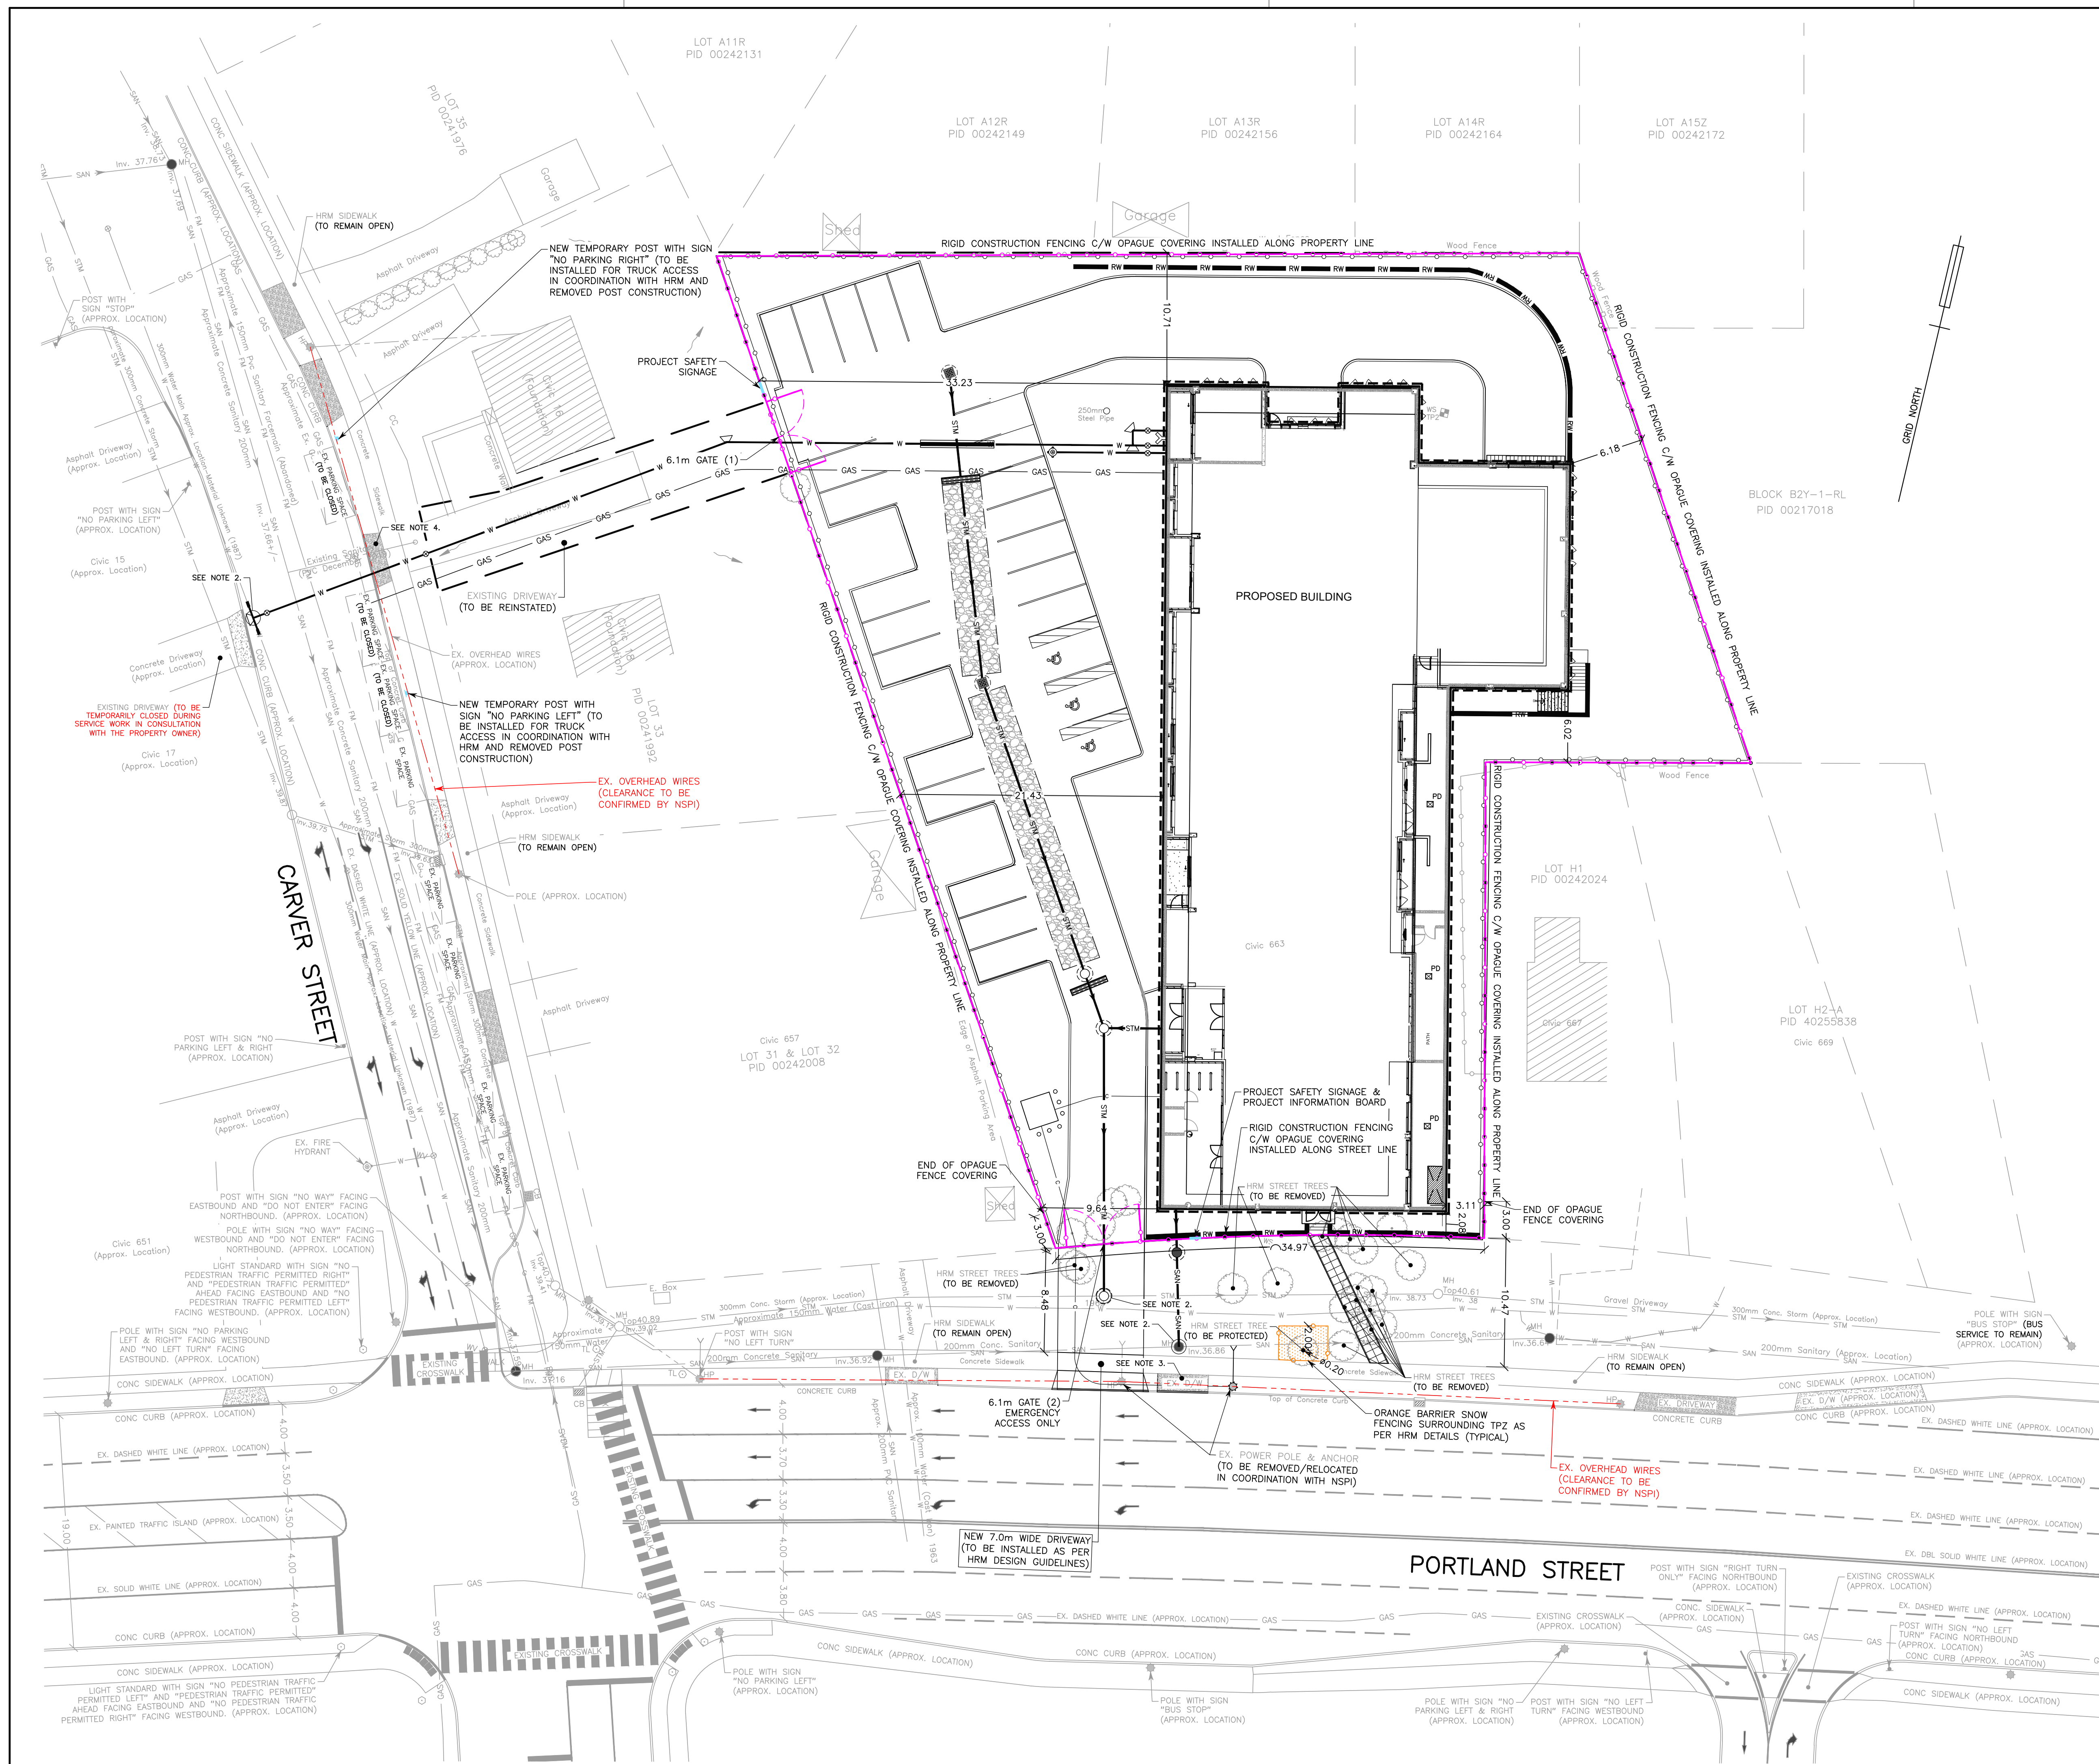

KEY PLAN

LEGEND

EXISTING	PROPOSED	
25.0	CONTOUR LINE	25.0
⊙/⊙BF	CURB STOP/GATE/BUTTERFLY VALVE	⊙/⊙BF
⊙	FIRE HYDRANT	⊙
⊙	CONCRETE THRUST BLOCK	⊙
⊙	SIAMSESE CONNECTION	⊙
⊙	CATCH BASIN/PIT	⊙
⊙	CULVERT	⊙
⊙	ROCK LINING/DAM	⊙
⊙	ROCK WALL/RETAINING WALL	⊙
⊙	POWER POLE & ANCHOR/LIGHT STANDARD	⊙
⊙	TREE	⊙
⊙	STREET SIGN/PARKING METER	⊙
⊙	ELEVATION/GRADE	125.00 x / 125.00
⊙	TEST PIT	⊙
⊙	DRAINAGE/SWALE FLOW DIRECTION	⊙
⊙	WATER MAIN/SERVICE	⊙
⊙	SANITARY MANHOLE & PIPE	⊙
⊙	STORM MANHOLE & PIPE	⊙
⊙	COMBINED PIPE	⊙
⊙	GAS LINE	⊙
⊙	100YR. FLOOD LIMIT	⊙
⊙	GUARD RAIL	⊙
⊙	UNDERGROUND CONDUIT	⊙
⊙	OVERHEAD WIRES	⊙
⊙	PROPERTY LINE/BOUNDARY	⊙
⊙	FENCE	⊙
⊙	BUILDING	⊙
⊙	TOP OF SLOPE	⊙
⊙	TOE OF SLOPE	⊙
⊙	TREELINE	⊙
⊙	LIMITS OF DISTURBANCE	⊙
⊙	TACTILE PEDESTRIAN PLATES	⊙
⊙	PROJECT SAFETY SIGNAGE	⊙
⊙	ORANGE SAWHORSE BARRICADE	⊙

- NOTES**
1. THIS PLAN IS IN METRIC.
 2. NEW SERVICE CONNECTIONS (REFER TO CIVIL PLANS).
 3. EXISTING DRIVEWAY CURB & RAMP TO BE REMOVED & REINSTATED WITH HIGH BACK CONCRETE CURB & GUTTER AND TOPSOIL & SOD AS PER HRM DESIGN GUIDELINES.
 4. EXISTING DRIVEWAY CURB & RAMP TO BE REINSTATED WITH CONCRETE SIDEWALK AS PER HRM DESIGN GUIDELINES.
 5. EXISTING CONDITIONS WITH APPROXIMATE LOCATIONS ARE BASED ON GOOGLE AERIAL IMAGERY AS SITE HAS NOT BEEN FIELD SURVEYED; DIMENSIONS MAY VARY AND SHALL BE CONFIRMED BY CONTRACTOR BEFORE PROCEEDING WITH CONSTRUCTION.


No.	YY/MM/DD	Revision	Description	Appr'd
1	24/07/25		REVISED AS PER CLIENT COMMENTS	
0	24/06/26		ISSUED FOR PERMIT	





PROPOSED APARTMENT BUILDING
663 PORTLAND STREET
DARTMOUTH, NOVA SCOTIA

PHASE 1 - ENCROACHMENT PLAN

Date	JUNE 26, 2024	Drawn	D. ANDERSON	Project No.	FILE NO. 1-7-135 (38410)
Scale	1:250	Engineer	G. MACLEAN	Plan No.	
Reference	--	Approved	G. MACLEAN	Drawing Name	R1-A
Surveyed	BY OTHERS	Sheet			



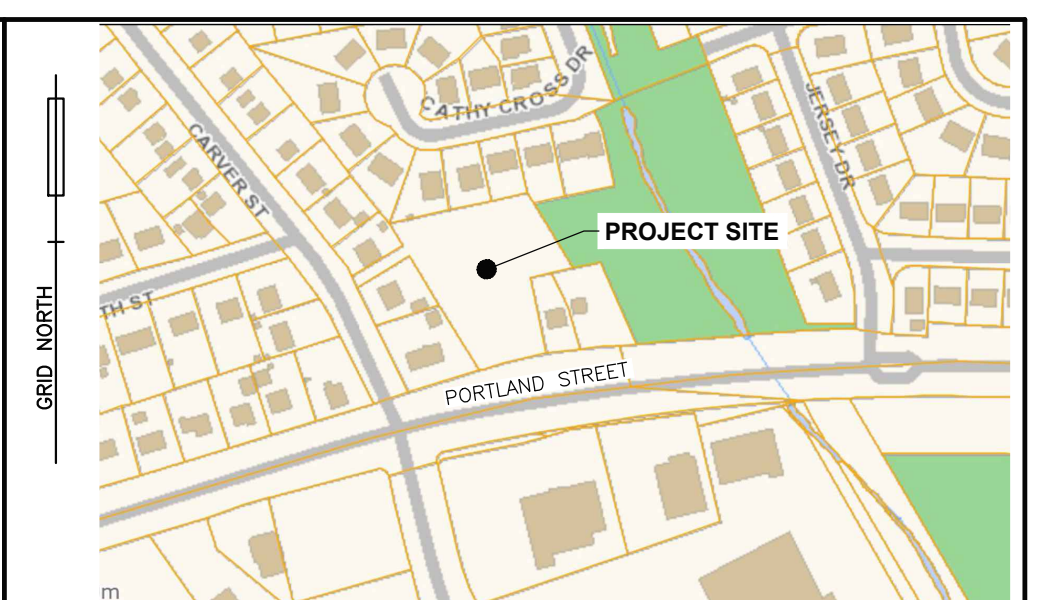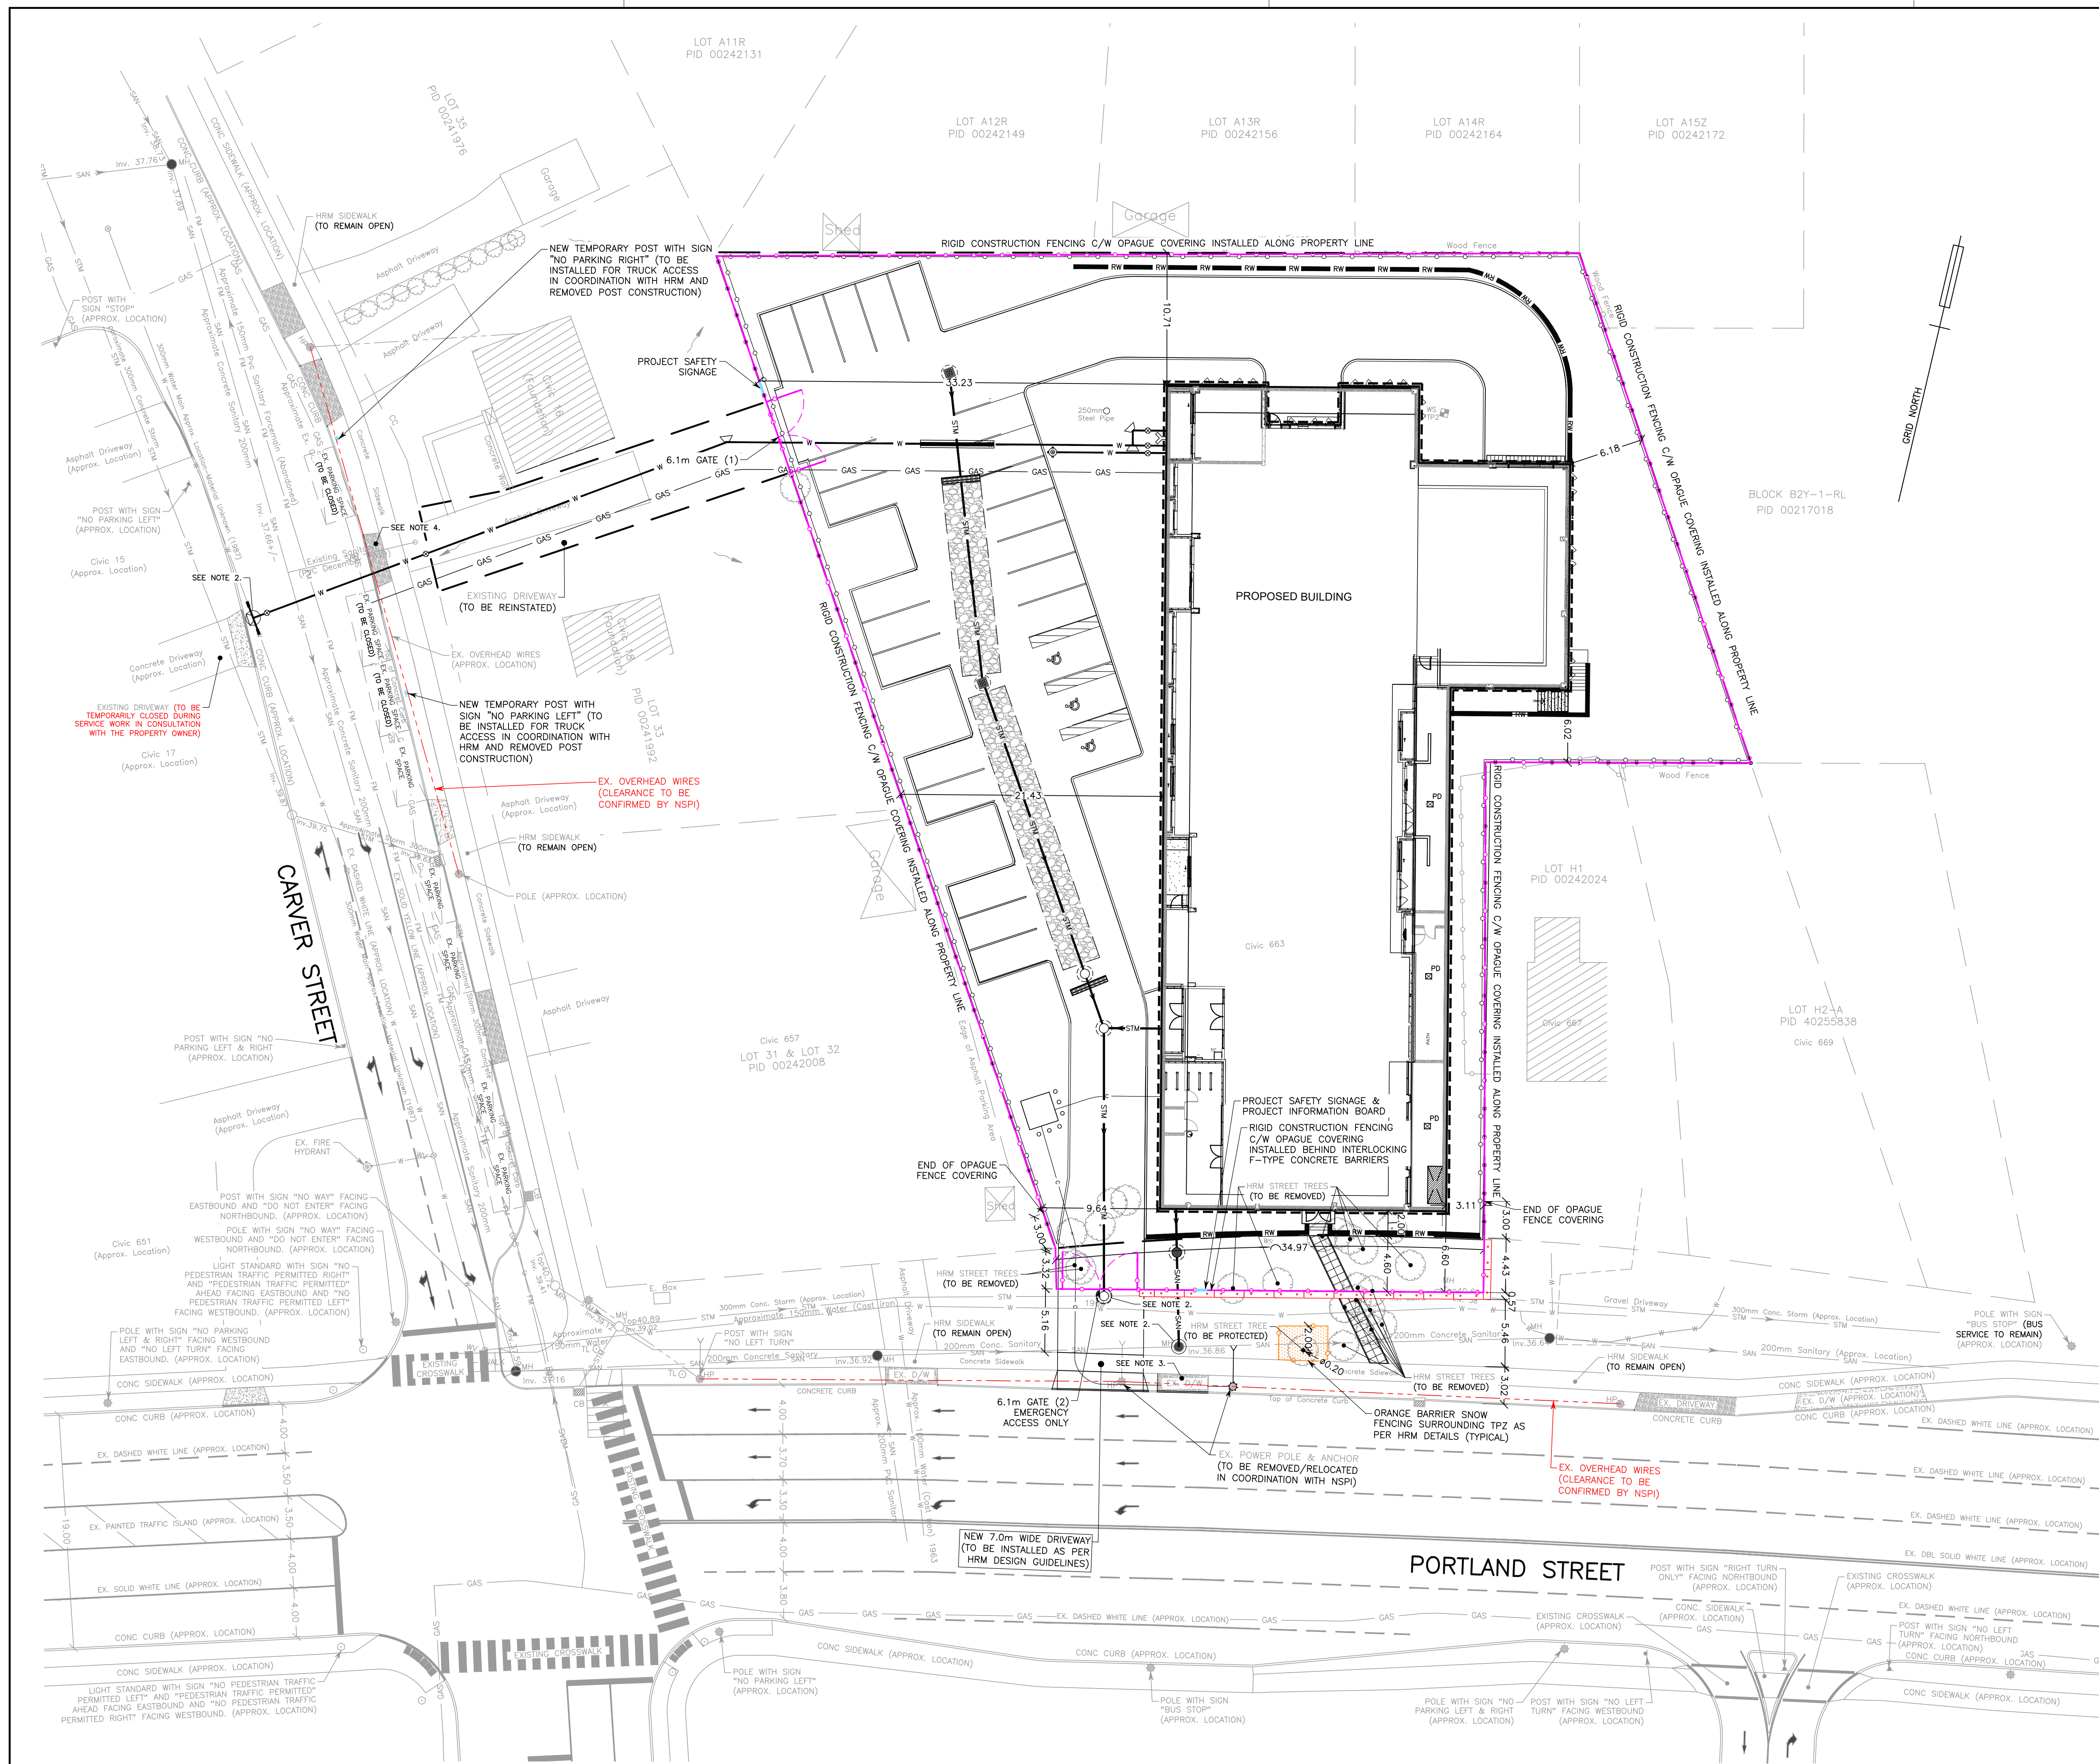

KEY PLAN

LEGEND

EXISTING	PROPOSED	
25.0	CONTOUR LINE	25.0
⊙/⊙BF	CURB STOP/GATE/BUTTERFLY VALVE	⊙/⊙BF
⊙	FIRE HYDRANT	⊙
⊙	CONCRETE THRUST BLOCK	⊙
⊙	SIAMSESE CONNECTION	⊙
⊙	CATCH BASIN/PIT	⊙
⊙	CULVERT	⊙
⊙	ROCK LINING/DAM	⊙
⊙	ROCK WALL/RETAINING WALL	⊙
⊙	POWER POLE & ANCHOR/LIGHT STANDARD	⊙
⊙	TREE	⊙
⊙	STREET SIGN/PARKING METER	⊙
⊙	ELEVATION/GRADE	125.00 x / 125.00
⊙	TEST PIT	⊙
⊙	DRAINAGE/SWALE FLOW DIRECTION	⊙
⊙	WATER MAIN/SERVICE	⊙
⊙	SANITARY MANHOLE & PIPE	⊙
⊙	STORM MANHOLE & PIPE	⊙
⊙	COMBINED PIPE	⊙
⊙	GAS LINE	⊙
⊙	100YR. FLOOD LIMIT	⊙
⊙	GUARD RAIL	⊙
⊙	UNDERGROUND CONDUIT	⊙
⊙	OVERHEAD WIRES	⊙
⊙	PROPERTY LINE/BOUNDARY	⊙
⊙	FENCE	⊙
⊙	BUILDING	⊙
⊙	TOP OF SLOPE	⊙
⊙	TOE OF SLOPE	⊙
⊙	TREELINE	⊙
⊙	LIMITS OF DISTURBANCE	⊙
⊙	TACTILE PEDESTRIAN PLATES	⊙
⊙	PROJECT SAFETY SIGNAGE	⊙
⊙	ORANGE SAWHORSE BARRICADE	⊙

- NOTES**
1. THIS PLAN IS IN METRIC.
 2. NEW SERVICE CONNECTIONS (REFER TO CIVIL PLANS).
 3. EXISTING DRIVEWAY CURB & RAMP TO BE REMOVED & REINSTATED WITH HIGH BACK CONCRETE CURB & GUTTER AND TOPSOIL & SOD AS PER HRM DESIGN GUIDELINES.
 4. EXISTING DRIVEWAY CURB & RAMP TO BE REINSTATED WITH CONCRETE SIDEWALK AS PER HRM DESIGN GUIDELINES.
 5. EXISTING CONDITIONS WITH APPROXIMATE LOCATIONS ARE BASED ON GOOGLE AERIAL IMAGERY AS SITE HAS NOT BEEN FIELD SURVEYED; DIMENSIONS MAY VARY AND SHALL BE CONFIRMED BY CONTRACTOR BEFORE PROCEEDING WITH CONSTRUCTION.

No.	YY/MM/DD	Revision Description	Appr'd
0	24/07/25	ISSUED FOR PERMIT	




SDMM
 Servant, Dunbrack, McKenzie & MacDonald Ltd.
 NOVA SCOTIA LAND SURVEYORS & CONSULTING ENGINEERS
 36 QUOND CRESCENT
 BERTS LAKE BUSINESS PARK
 HALIFAX, NS B3S 1C6
 PHONE: (902) 455-1537
 FAX: (902) 455-9479
 WEB: www.sdmm.co

PROPOSED APARTMENT BUILDING
 663 PORTLAND STREET
 DARTMOUTH, NOVA SCOTIA

PHASE 2 - ENCROACHMENT PLAN

Date	July 25, 2024	Drawn	D. ANDERSON	Project No.	FILE NO. 1-7-135 (38410)
Scale	1:250	Engineer	G. MACLEAN	Plan No.	
Reference	--	Approved	G. MACLEAN	Drawing Name	R1-B
Surveyed	BY OTHERS	Sheet			




Appendix B – Traffic Control Plans TCP


Encroachment Signage Plan

Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374

Comments:
Not to Scale
Encroachment Signage Plan
Off Shoulder Work Area




Legend	
	Gate
	Sanitary Lateral
	Site Fencing
	Storm Lateral
	Water Lateral

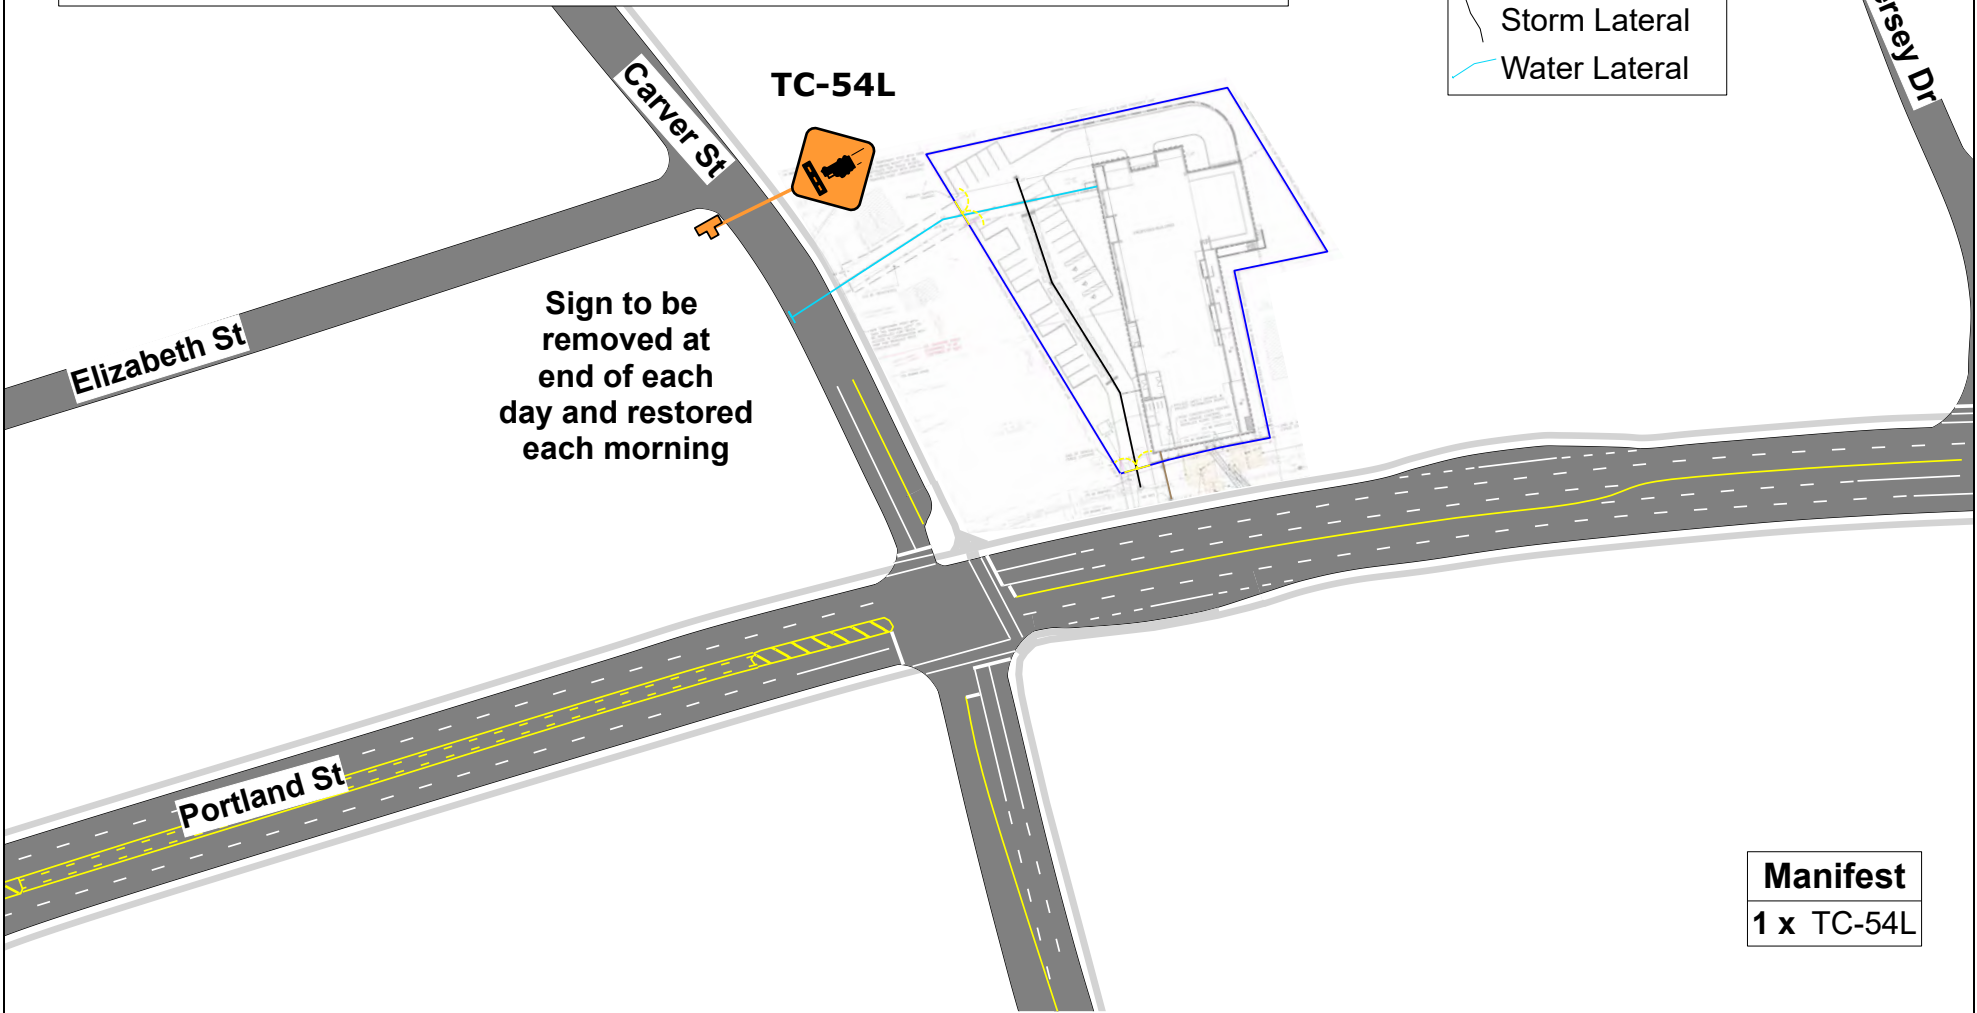

Sign to be removed at end of each day and restored each morning

Manifest
1 x TC-54L


General Traffic Control Plan



Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374
Comments:
 Not to Scale
 General Traffic Control Plan
 Use this plan for all activities that must take place along Portland St, Including:
 Sanitary and Storm Laterals, driveway, curb and sidewalk renewal
 Application Guide A63R
 Sidewalk closure required. see PMP 1 for sidewalk closure details

Legend

- Barrel
- Gate
- Sanitary Lateral
- Site Fencing
- Storm Lateral
- Water Lateral
- Work Area

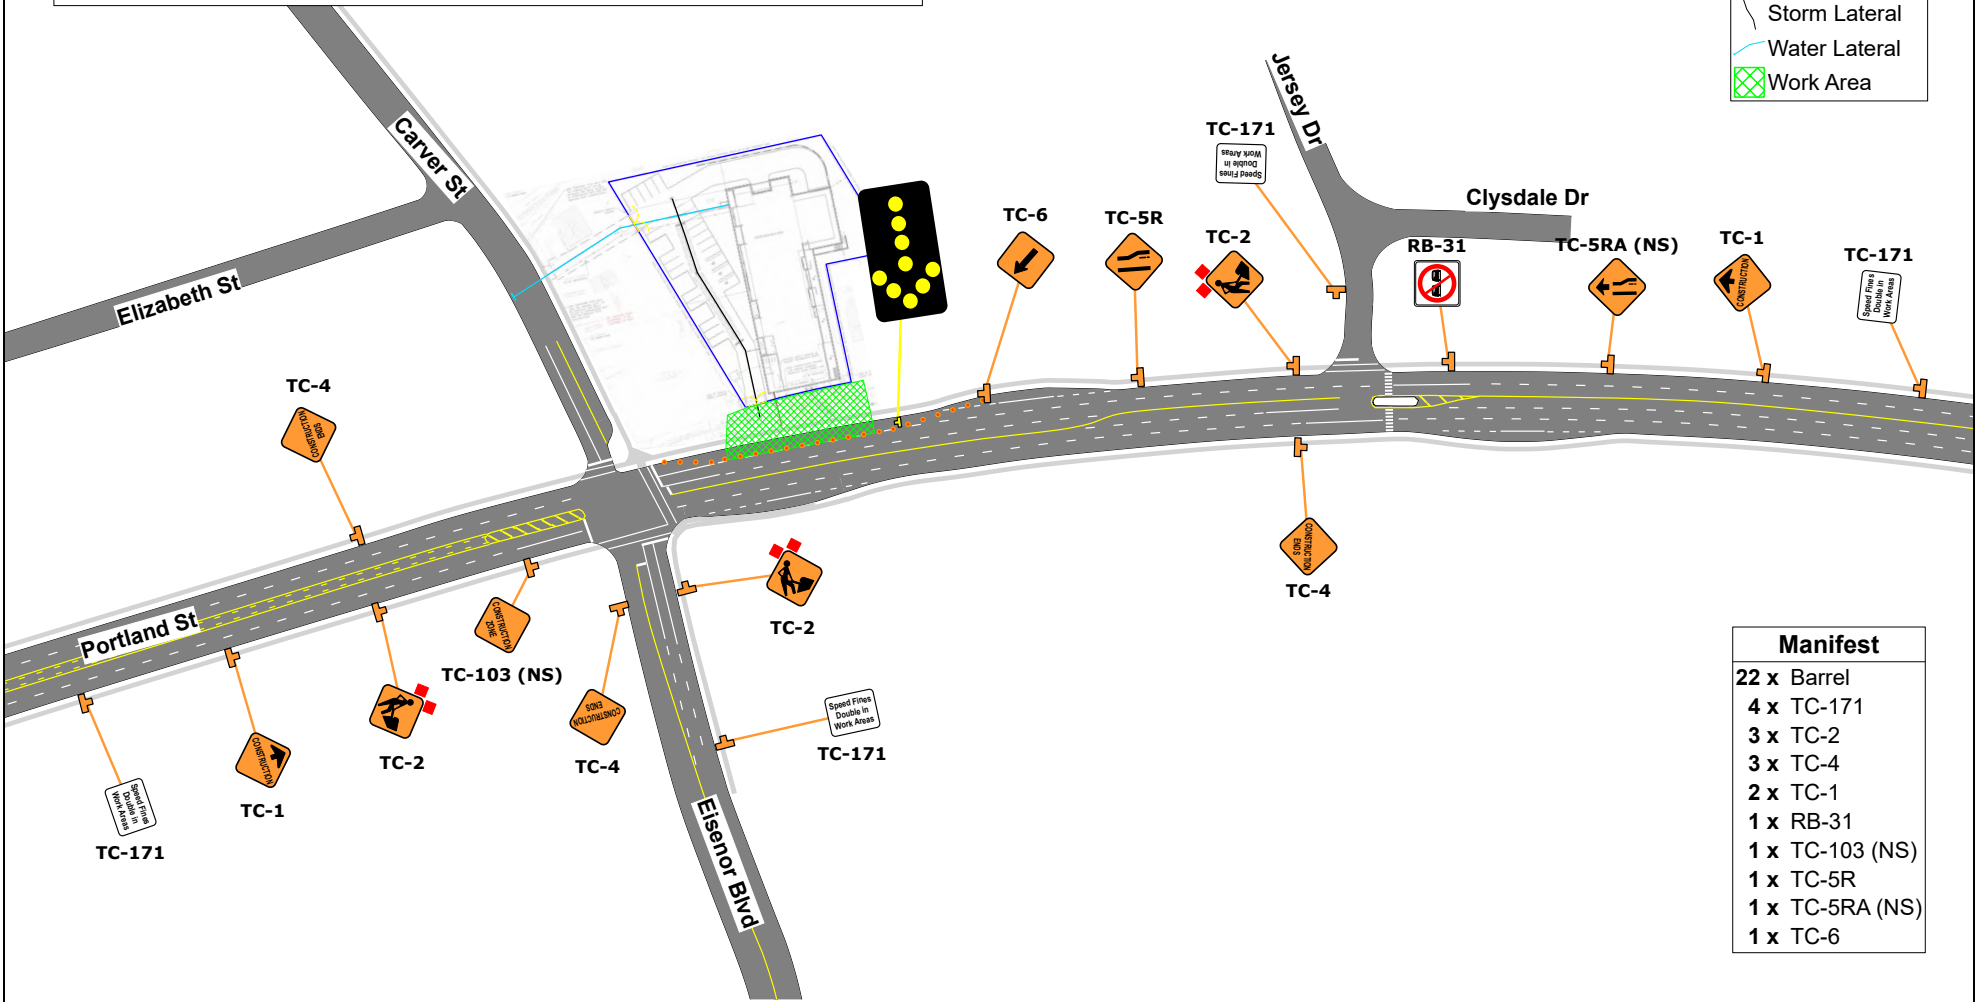

Manifest


22 x Barrel
4 x TC-171
3 x TC-2
3 x TC-4
2 x TC-1
1 x RB-31
1 x TC-103 (NS)
1 x TC-5R
1 x TC-5RA (NS)
1 x TC-6

General Traffic Control Plan for Carver St



Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374
Comments:
 Not to Scale
 General Traffic Control Plan for Carver St.
 Application Guide C22
 Use this plan for all construction activities that require road access.
 See Pedestrian Management Plan 2 for sidewalk closure details

Legend	
	Barrel
	Cone
	Gate
	Sanitary Lateral
	Site Fencing
	Storm Lateral
	Water Lateral
	Work Area

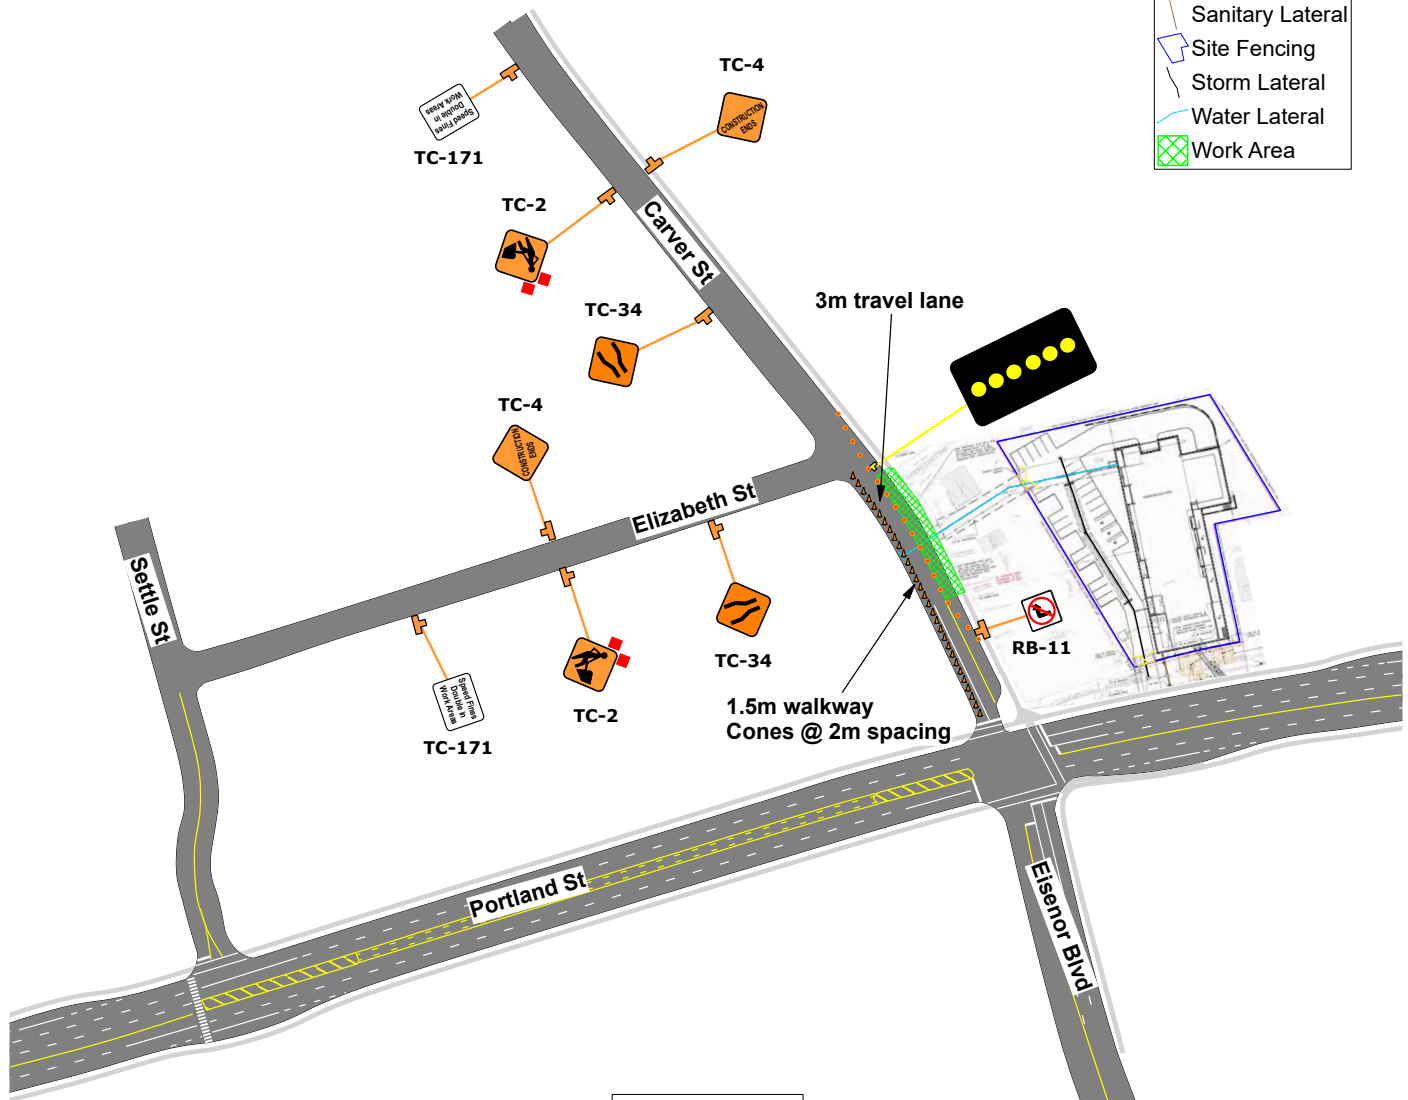


Manifest	
30 x	Cone
18 x	Barrel
2 x	TC-171
2 x	TC-2
2 x	TC-34 TC-34
2 x	TC-4
1 x	RB-11 RB-11

Water Lateral Installation Plan 1



Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374
Comments:
 Not to Scale
 Water Lateral Installation Plan
 Application Guide C22
 Residents and spa visitors must be notified that it will not be possible to turn Northbound on Carver while work is being conducted. A temporary walkway must be established along opposing curb to give pedestrians a place to walk. TCP on site to assist those trying to get through the site

Legend	
	Barrel
	Cone
	Gate
	Sanitary Lateral
	Site Fencing
	Storm Lateral
	Water Lateral
	Work Area

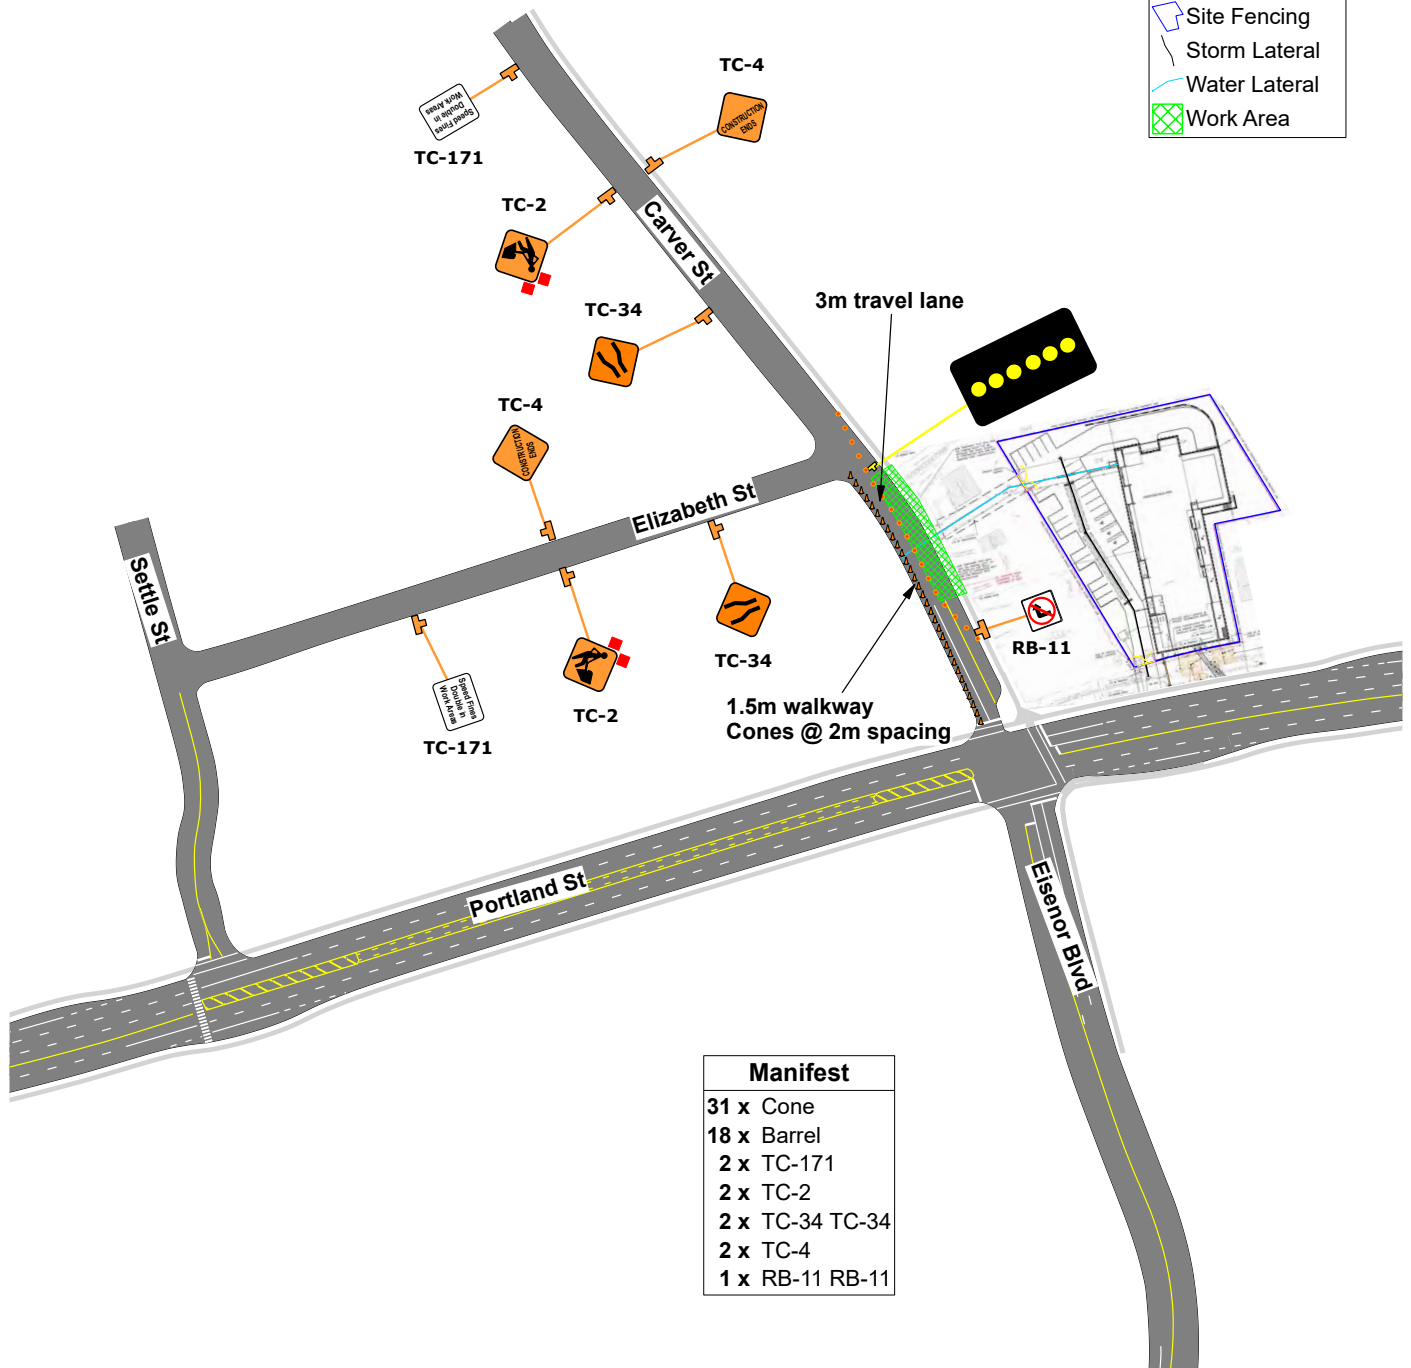


Manifest	
31 x	Cone
18 x	Barrel
2 x	TC-171
2 x	TC-2
2 x	TC-34 TC-34
2 x	TC-4
1 x	RB-11 RB-11

Water Lateral Installation Plan 2



Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374
Comments:
 Not to Scale
 Water Lateral Installation Plan
 Application Guide C22
 Residents and spa visitors must be notified that it will not be possible to turn Northbound on Carver while work is being conducted. Sidewalk must be open to public use before this plan can be used


Legend	
	Barrel
	Gate
	Sanitary Lateral
	Site Fencing
	Storm Lateral
	Water Lateral
	Work Area

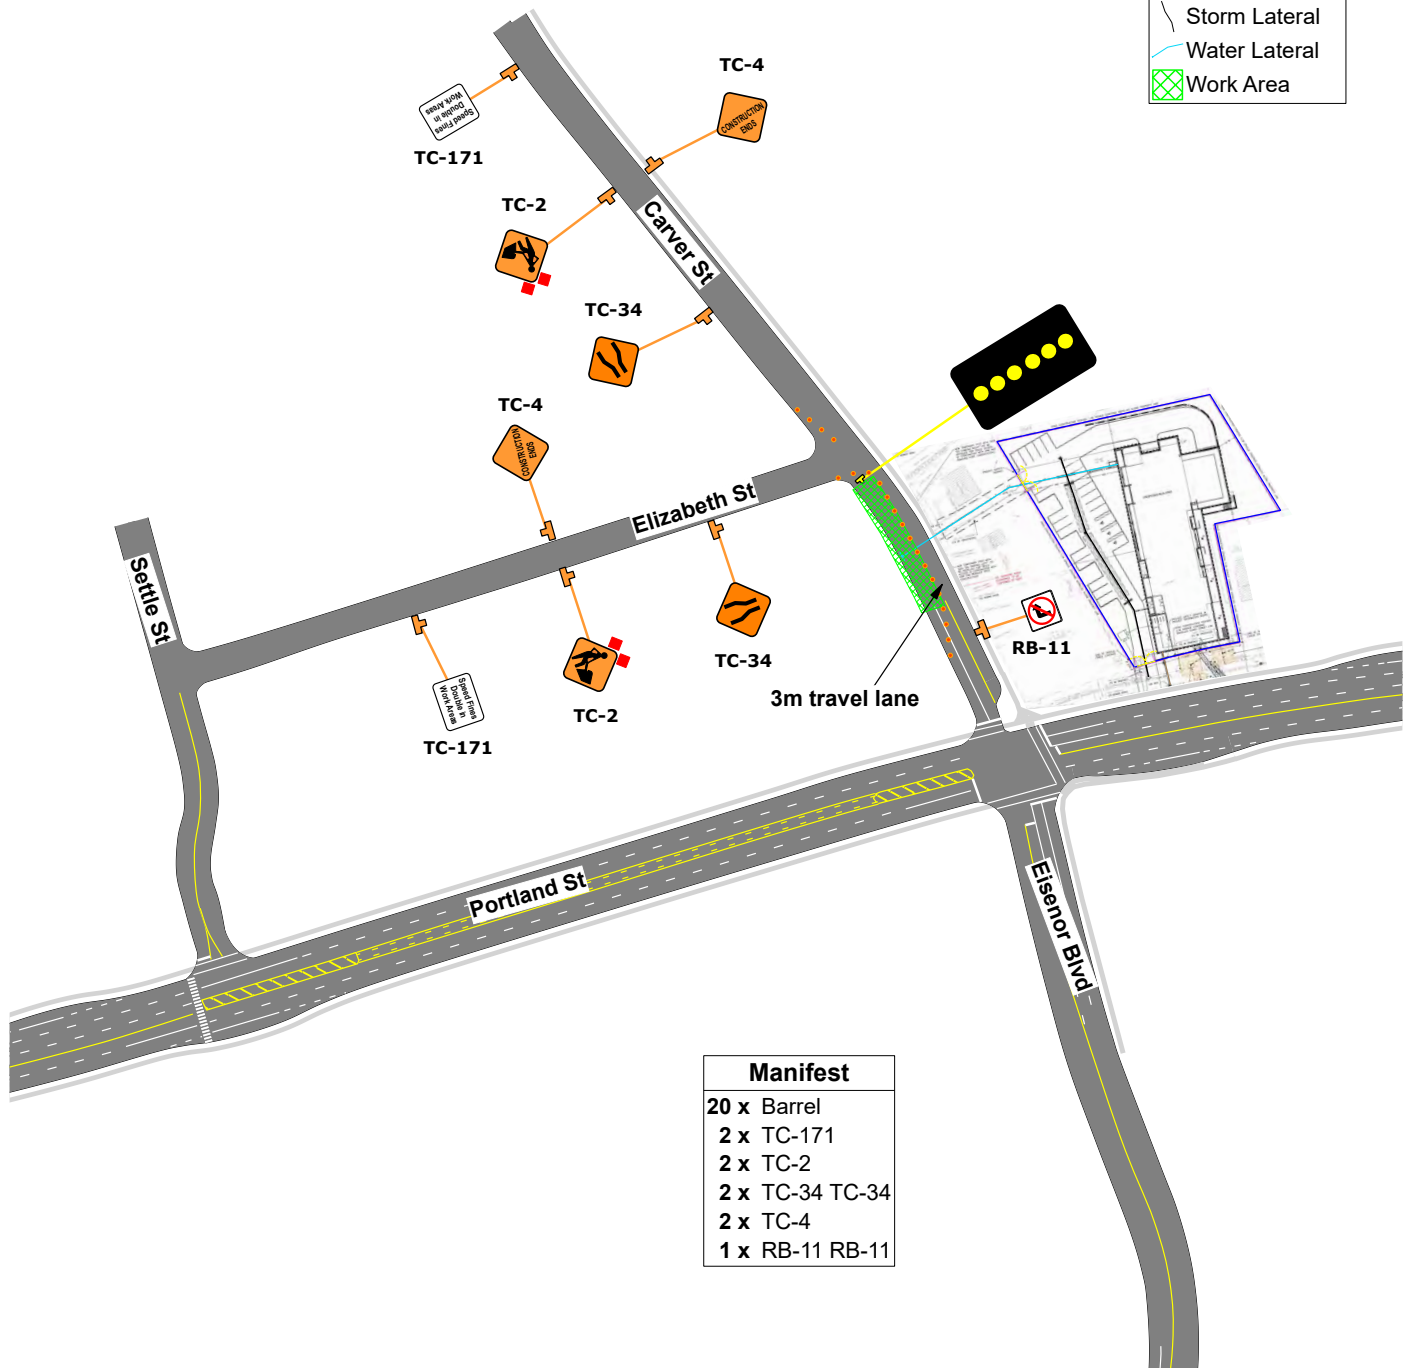

Manifest	
20 x	Barrel
2 x	TC-171
2 x	TC-2
2 x	TC-34 TC-34
2 x	TC-4
1 x	RB-11 RB-11

Appendix C – Haul Route Plan

Haul Route Plan




Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374

Comments:



Not to Scale

Inbound Via Hwy 111 to Portland St to Woodlawn Rd to Day Ave to Carver St

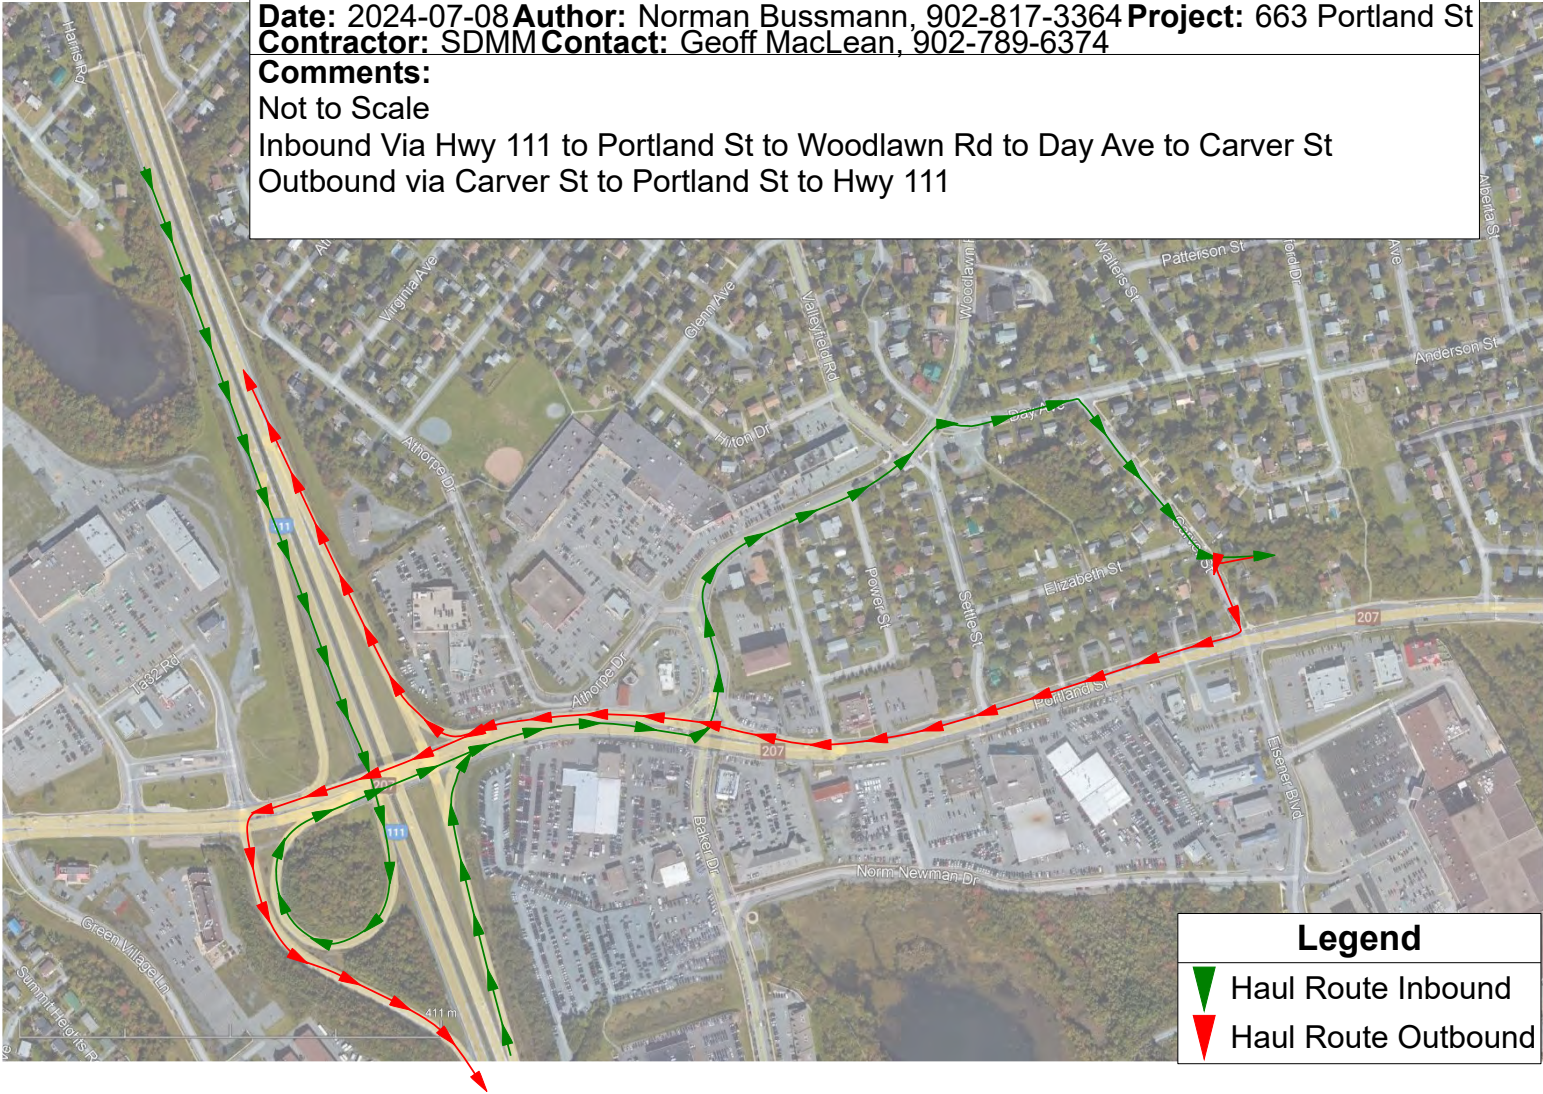Outbound via Carver St to Portland St to Hwy 111



Legend


-  Haul Route Inbound
-  Haul Route Outbound

Appendix D – Pedestrian Management Plan (PMP)


Pedestrian Management Plan 1

Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374

Comments:
Not to Scale
Pedestrian Management Plan 1 for Portland St sidewalk closure




Legend	
	Pedestrian Pathway

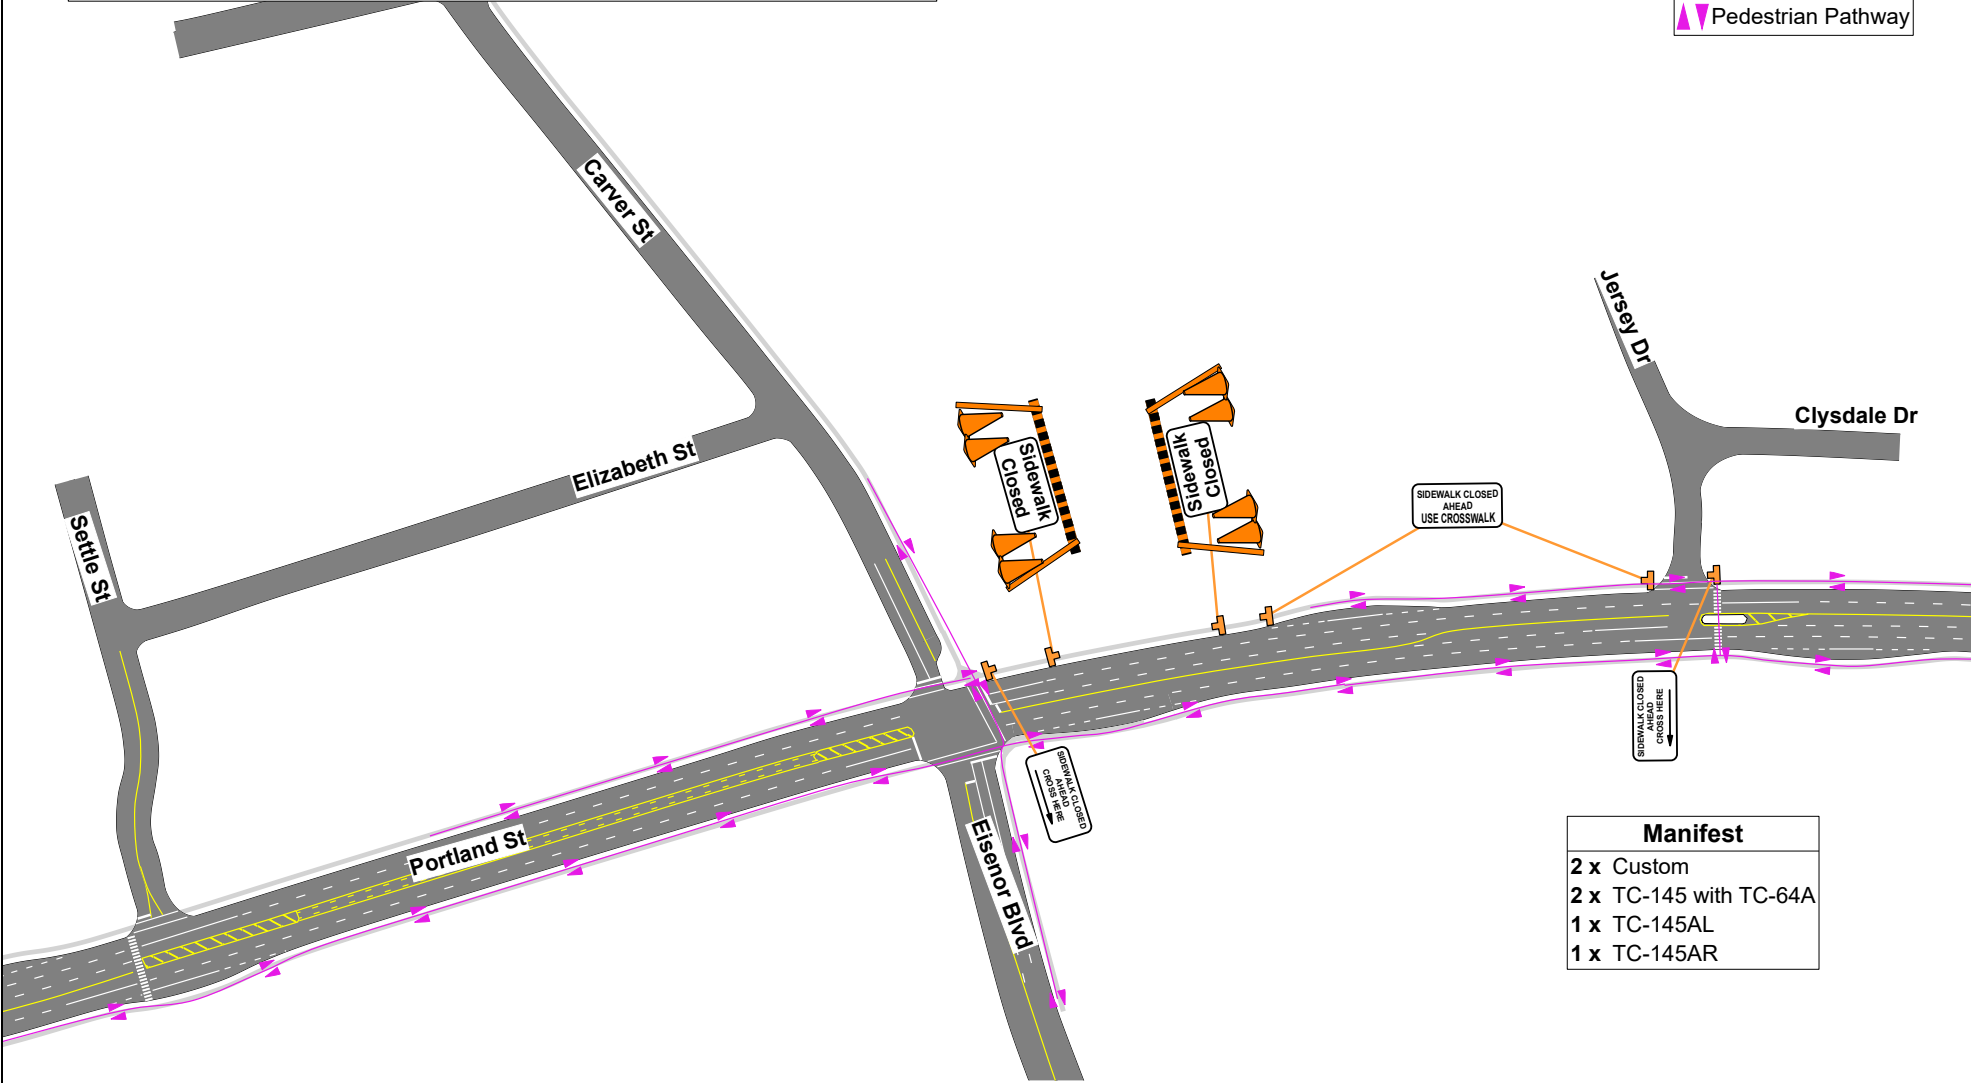


Manifest	
2 x Custom	
2 x TC-145 with TC-64A	
1 x TC-145AL	
1 x TC-145AR	

Pedestrian Management Plan 2



Date: 2024-07-08 **Author:** Norman Bussmann, 902-817-3364 **Project:** 663 Portland St
Contractor: SDMM **Contact:** Geoff MacLean, 902-789-6374
Comments:
 Not to Scale
 Pedestrian Management Plan 2 for Carver St sidewalk closure



Legend	
	Barrel
	Cone
	Gate
	Pedestrian Pathway
	Sanitary Lateral
	Site Fencing
	Storm Lateral
	Water Lateral
	Work Area

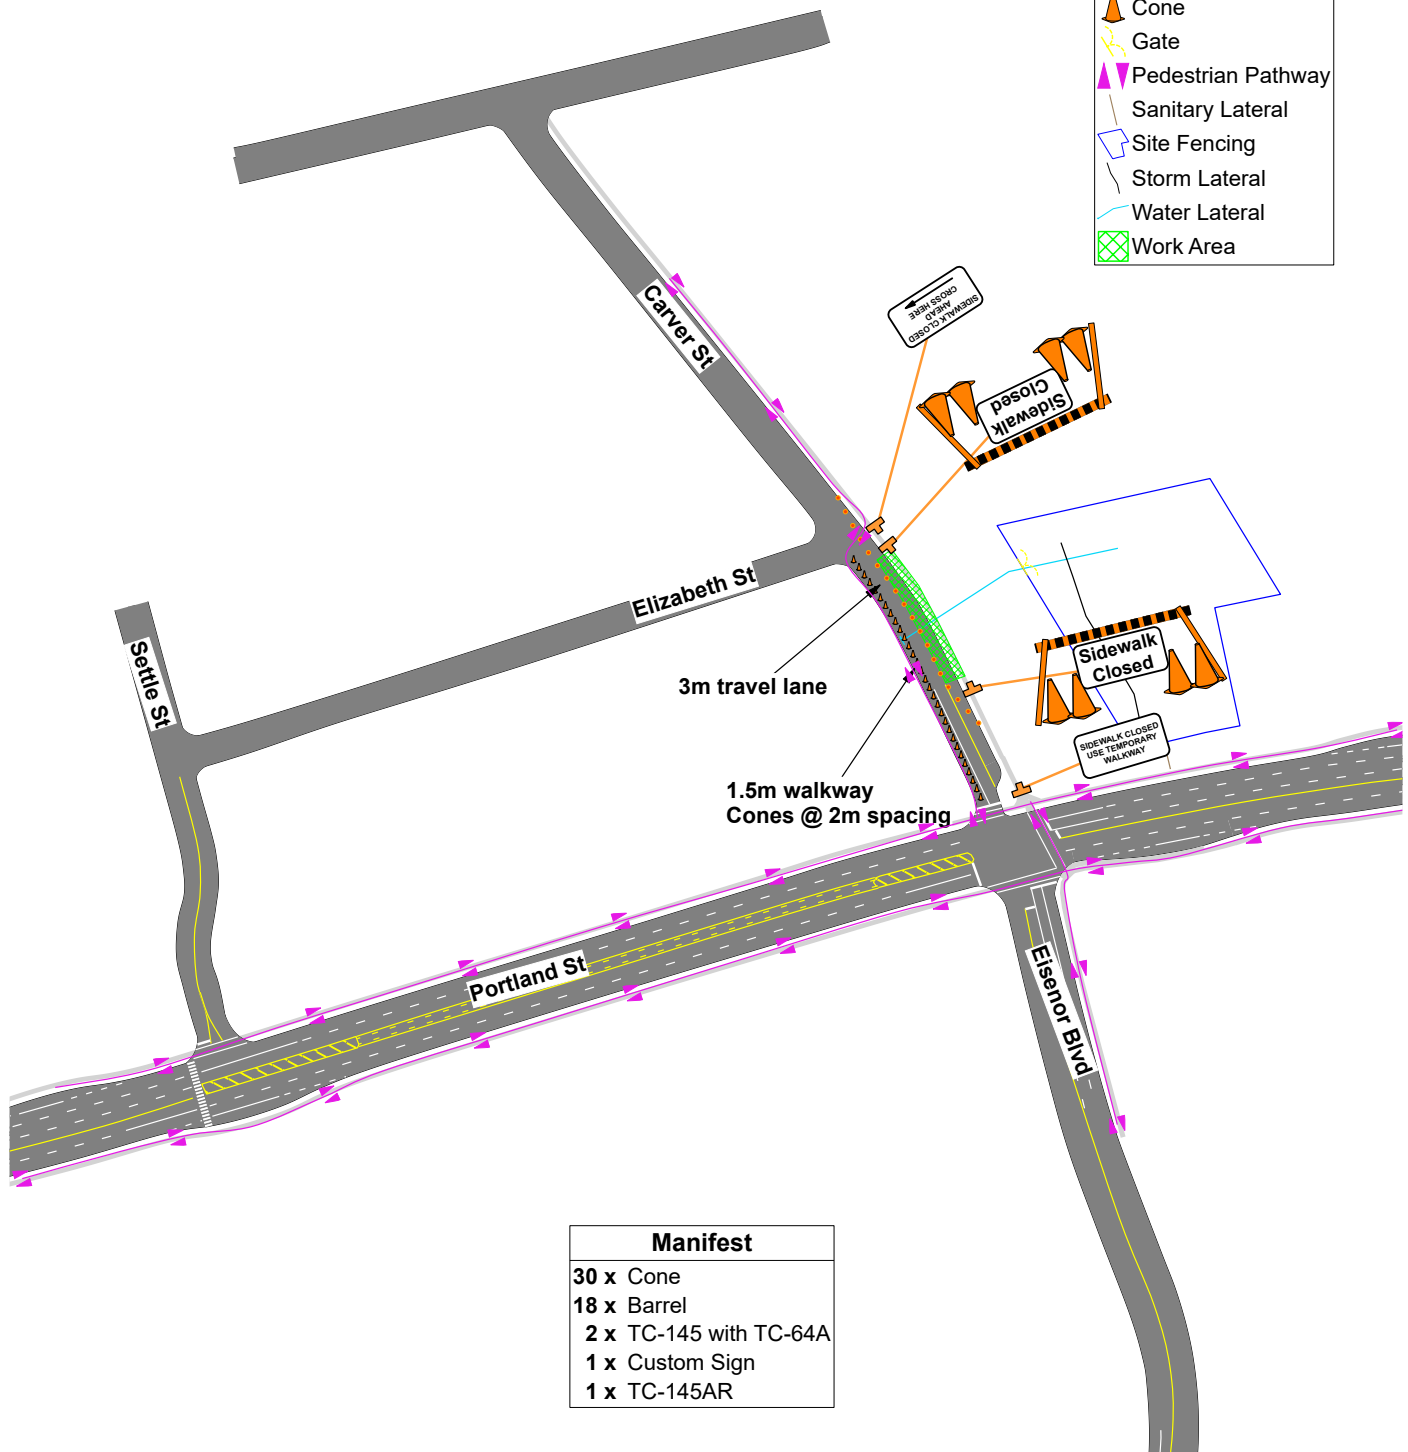


Manifest
30 x Cone
18 x Barrel
2 x TC-145 with TC-64A
1 x Custom Sign
1 x TC-145AR

Appendix E – Fence & Gates Information


Sample Barrier & Fence Details

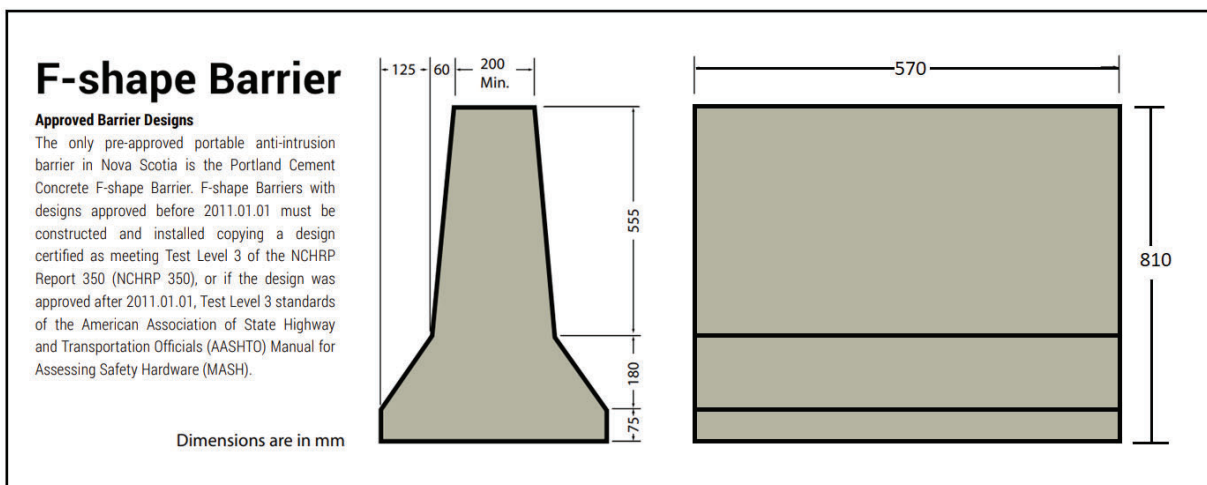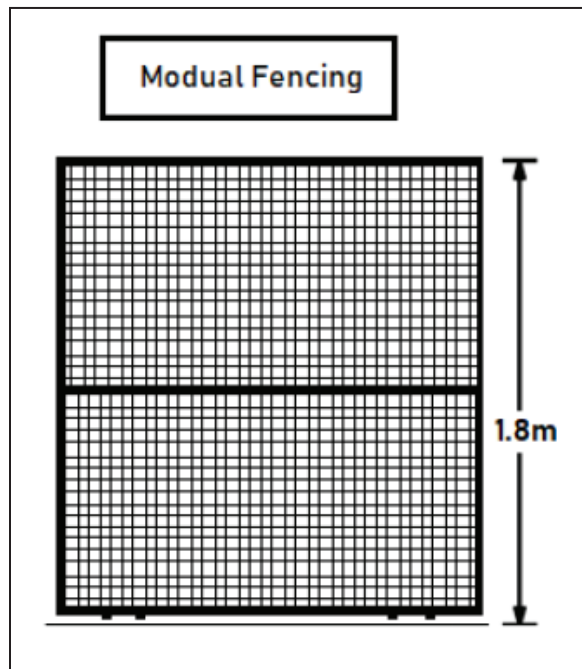

Fence anchored to the ground behind interlocking F-type concrete barriers

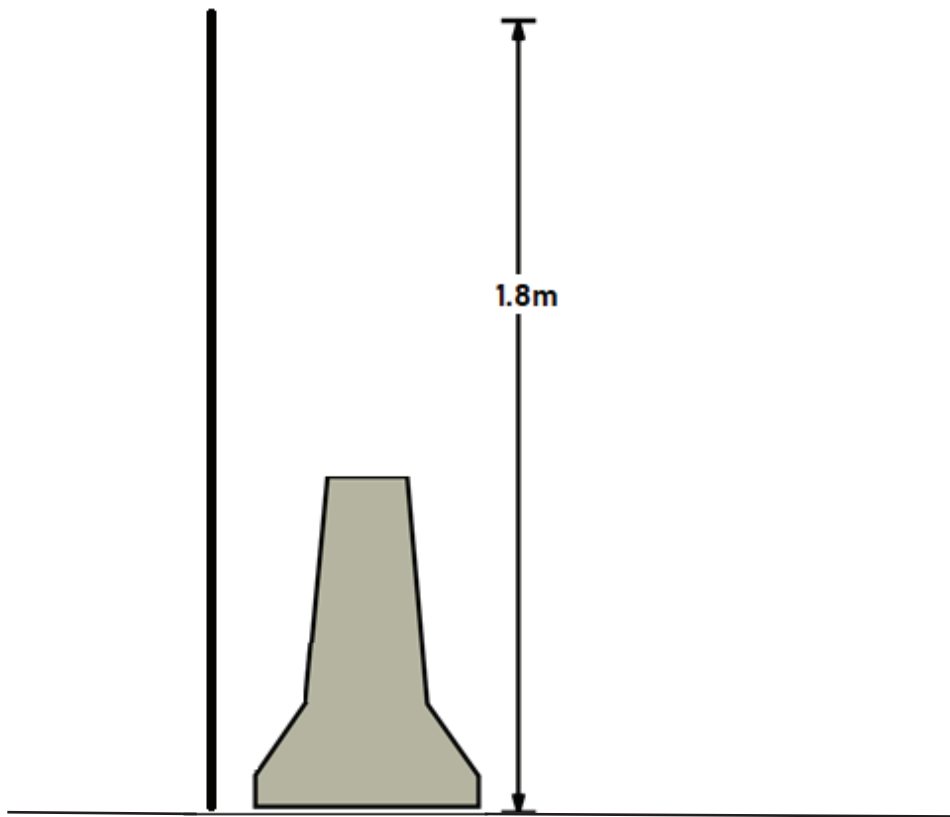

Sample Gate Detail

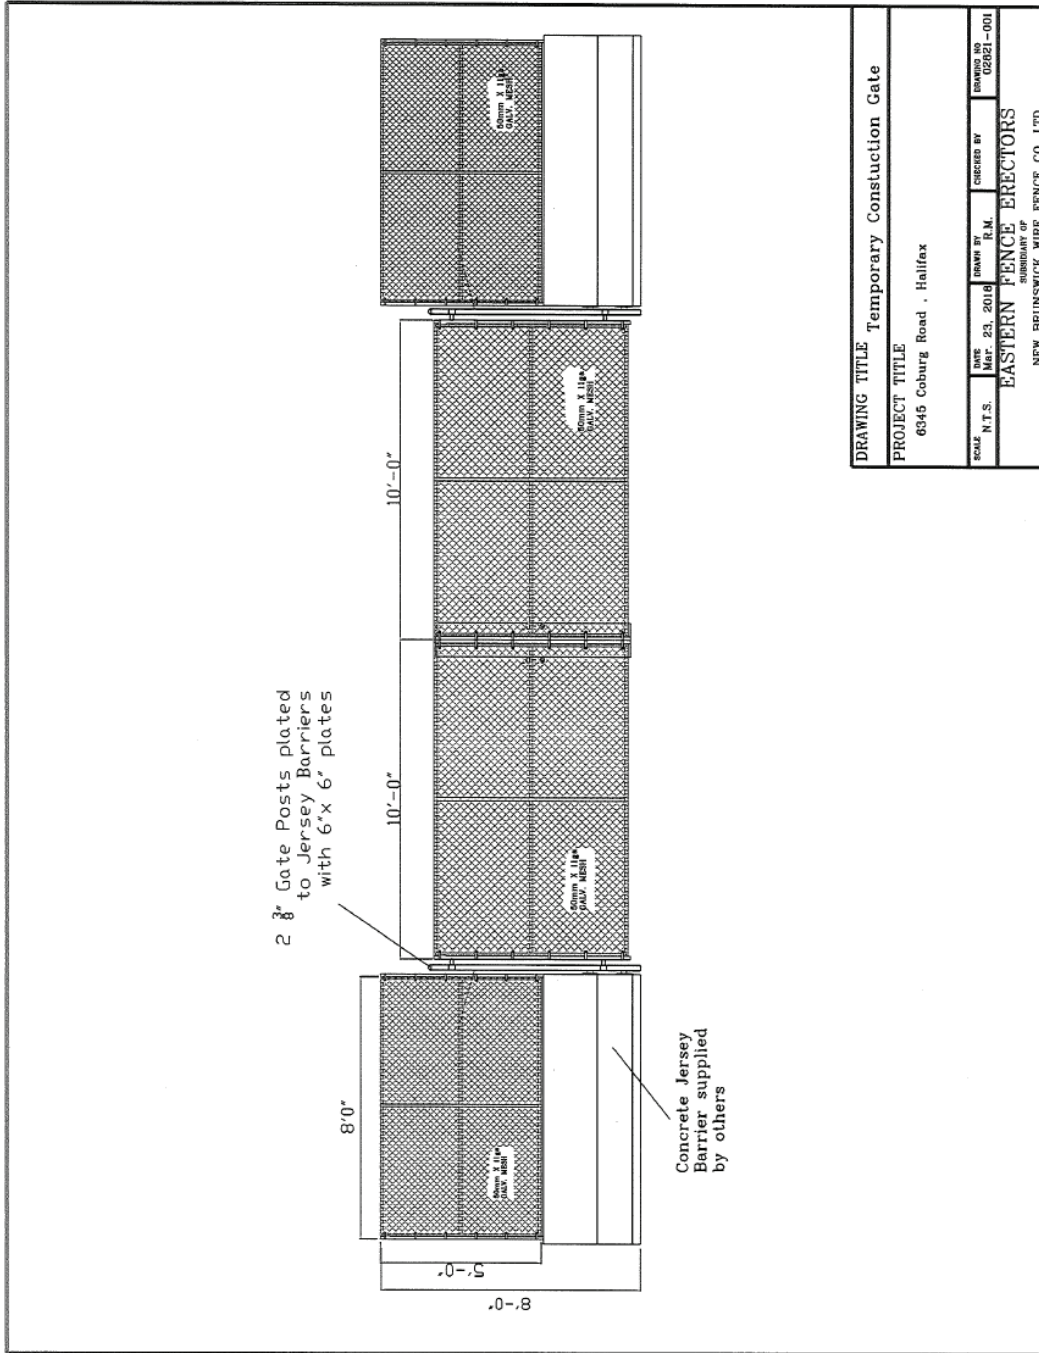

Appendix F – Hoarding Information

Opaque construction hoarding material shall covering and be adequately secured to the rigid fencing that outlines the encroachment area. This covering shall be continuous such that it prevents passersby or tourist from seeing through the fencing and gates to the active construction site.

UltraMesh® Eclipse® if a 7.96 oz. which is a polyester, black-backed mesh that is used where complete opacity is required.

UltraMesh Eclipse is UV printable for project renderings and is typically used for building and fence graphic wraps. The product is available in widths of 126" and 196".

Product example is shown below with the technical data sheet on the following page.

Tarp Option



Print Banner Option



UltraMesh Eclipse is a 7.96 oz. polyester, black-backed mesh. The material is ideal for applications where complete opacity is required. UltraMesh Eclipse is UV printable and may be used for building wraps and fence graphics. Available in widths of 126 and 196 .

Material Details

CHARACTERISTICS	TEST METHOD	METRIC	ENGLISH
Base Fabric	100% PES	1000D×1000D	
Construction			12×12
Total Weight	DIN53352 BS3424 Method5A	270 +/- 20 gsm/m ²	7.96 oz/yd ²
Width		Up to 500cm	
Tensile Strength	DIN53352 BS3424	Warp 1250 n/5cm Weft 1100 n/5cm	142.75 x 130.19 lb/in
Tear Strength	DIN53356 BS3424	Warp 235 N Weft 225 N	52.8 x 50.5 lbf
Air Permeability	GB/T 2410-2008		2649 mm/s
Light Transmission	GB/T 5453-1997		37%
Temperature Resistance	DIN53357 BS3425 Method 10		-20°C /70°C

Applications

	Back-lit	Banner	Billboard	Block-out	Building Wrap	Fence Graphics	Truckside
Applications		■		■	■	■	

Ink Printability

Solvent	Eco Solvent	UV	Latex	Screen Printing	Dye Transfer	Dye Direct
		■				

Available Sizes

Metric (m)	English (inches)
3.20, 5.00	126 , 196

The information on physical and chemical characteristics is based upon tests believed to be reliable. The values are intended only as a source of information. A legally binding guarantee of specific properties is not to be inferred from our specifications. They are given without guaranty and do not constitute a warranty. A weight variance of +1/-2 is acceptable. The purchaser should independently determine, prior to use, the suitability of this material for his/her specific purpose. (Data represents averages and is not intended for use as a specification.)

Appendix G – Project Information Board



August 2024 – January 2026

**PORTLAND & CARVER APARTMENTS
663 Portland Street**

6 Storey – Residential Building

81 Residential Units on 6 Levels

Level 1 Commercial Space

1, 2, and 2 Bedroom plus Den Units

Level 5 & 6 Outdoor Amenity

2 Levels of Underground parking with
Surface Level parking

Developer:

Mayabella Homes
11 Kelvin Grove, Halifax, NS

Contact:

Johnny Anjoul – (902) 209-6902 (24hr contact)

Site Contractor:

Atlantic Road Construction and Paving
6 Belmont Avenue, P.O. Box 89, Eastern Passage, NS, B3G 1M7

Contact:

Greg MacDonald – (902) 830-6411

Traffic Control:

Frontline Traffic Services
6 Belmont Avenue, P.O. Box 89, Eastern Passage, NS

Contact:

Tyler Hayman – (902) 818-5548

Rodent Control Company:

Rentokil Pest Control
51 Duke Street, Bedford, Bedford, NS

Contact:

Main Office – 902- 835-2304

Appendix H – Project Safety Signage



RESTRICTED
— AREA —


CONSTRUCTION
WORK IN
PROGRESS

Appendix I – Project Signage Specifications

Signage Specifications: Project Signage shall;

- Be constructed of weatherproof material (corrugated plastic)
- Have high visibility contrasting colours (dark letters on white background)
- Incorporate appropriate font types (mix of upper and lower-case lettering)
- Incorporate appropriate font sizes (16mm – 51mm) such that the signage is readable from a distance (16-20m)
- Size of signage will be poster size (600mm x 900mm) or larger; to allow community members to see and read the information from a distance
- Signage may incorporate plastic grommets positioned every 300mm around the perimeter of the signage to ensure a secure signage installation
- Signage will be installed/anchored to project fencing using plastic zip-ties
- Signage will be positioned along the project site as per the encroachment plan
- Signage shall not impede traffic of pedestrian sight lines
- **Signage shall be placed on site 10 days prior to the start of the noted construction activity to ensure the passing public has had adequate time to review, adjust their travel patterns, usage of streets and or can be considered 'informed'.**

Samples

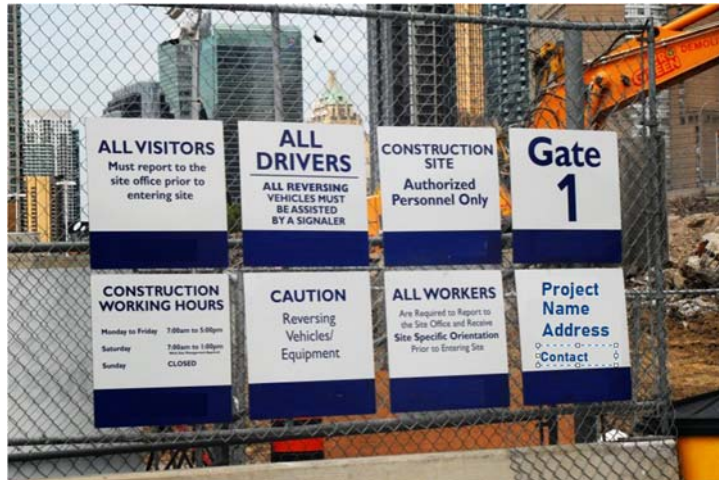

Appendix J – Sample Traffic Notification Letter



Proposed Multi-Unit Residential Building

DRAFT NOTIFICATION LETTER

TO WHOM IT MAY CONCERN

Date

NOTIFICATION OF TRAFFIC DISRUPTION: STREET NAME, DARTMOUTH, NOVA SCOTIA

This is to inform you that the to facilitate operations in association with the building construction work, traffic disruptions will occur on or about **DATE** with an anticipated duration of approximately **TIME**. The street will be **reduced(?)** to one lane of vehicular traffic during this time.

Should you have any questions or concerns please feel free to contact the below:

CONTACT INFORMATION

Site Contractor:

Atlantic Road Construction and Paving

6 Belmont Avenue, P.O. Box 89

Eastern Passage, NS, B3G 1M7

Phone: (902) 830-6411

Should any questions arise, please feel free to contact the undersigned.

Yours Truly,

Greg MacDonald

Atlantic Road Construction and Paving.

Appendix K – Vehicular and Pedestrian Hazard Assessment

Project

Date:

Location:

VEHICULAR & PEDESTRIAN HAZARD ASSESSMENT

No.	Hazard:	Project Phase:	Vehicular Impacts:	Mitigation Methods:	Pedestrian Impacts:	Mitigation Methods:
1	Excavation	Excavation	Vehicles may enter project site and fall down excavation.	Place concrete barriers along travel ways. Concrete barriers and existing curbs to prevent vehicle entry.	Pedestrians may enter project site and fall down excavation.	Place concrete barriers/rigid fencing around entire project site.
			Vehicle weight may surcharge excavation, causing excavation wall failure.	Close sidewalks & driveways adjacent to project site, moving vehicles farther away from excavation.		
2	Rock Blasting	Excavation	Blasted rock projectiles may strike vehicles.	Close sidewalks & driveways adjacent to site, moving vehicles farther away from blasted rock.	Blasted rock projectiles may strike pedestrians.	Install solid plywood hoarding along rigid fence adjacent to blasting zone.
3	Construction Waste	All Phases	Vehicles may be struck by construction waste.	The contractor shall keep the project site and surrounding areas clean and free of construction debris.	Pedestrians may be struck by construction waste.	The contractor shall keep the project site and surrounding areas clean and free of construction debris.
4	Vehicular & Pedestrian Activities	All Phases	Drivers and pedestrians may become confused or impatient with construction activities. Pedestrians may walk in unmarked crosswalks or in vehicular travel areas. Drivers may fail to obey traffic signage.	Vehicular and pedestrian signage will be posted prominently around the project site to facilitate pedestrian movement. Notification will be sent prior to all traffic interruptions.	Drivers and pedestrians may become confused or impatient with construction activities. Pedestrians may walk in unmarked crosswalks or in vehicular travel areas. Drivers may fail to obey traffic signage.	Vehicular and pedestrian signage will be posted prominently around the project site to facilitate pedestrian movement. Notification will be sent prior to all traffic interruptions.
5	Heavy Machinery Operation	All Phases	Heavy machinery or vehicles may break down or overturn, damaging other vehicles.	The contractor shall maintain safe distances between vehicles and heavy machinery on-site. Concrete barriers will be installed to separate construction vehicles from public traffic.	Heavy machinery or vehicles may break down or overturn, injuring pedestrians.	The contractor shall maintain safe distances between pedestrians, vehicles, and heavy machinery. Rigid fences will be installed to separate construction vehicles from pedestrians.
			Heavy machinery or vehicles may overturn due to uneven terrain, damaging other vehicles.	The contractor shall maintain safe distances between vehicles and heavy machinery on-site and ensure travel routes are kept flat.	Heavy machinery or vehicles may overturn due to uneven terrain, injuring pedestrians. Pedestrians may walk on uneven terrain causing them to twist their ankles or fall.	The contractor shall maintain safe distances between pedestrians, vehicles, and heavy machinery and ensure travel routes are kept flat.
6	Construction Signage	All Phases	Construction signage may strike vehicular traffic.	Construction signage will be securely fixed to existing poles, temporary concrete sign bases, or rigid fences.	Pedestrians may walk into construction signage, including traffic signage, wayfinding signs, etc. may.	Signage will be angled in line with pedestrian routes and/or be placed at heights such that they do not pose a risk to pedestrians.
					Construction signage may strike pedestrians.	Construction signage will be securely fixed to existing poles, temporary concrete sign bases, or rigid fences.
7	Dangerous Materials	All Phases	Flammable, explosive, & hot materials may damage vehicles if not properly maintained & stored.	The contractor will use and store dangerous materials properly as per manufacturers' specifications.	Flammable, explosive, & hot materials may injure pedestrians if not properly maintained & stored.	The contractor will use and store dangerous materials properly as per manufacturers' specifications.
8	Hoisting Operations	Superstructure	Precast concrete panels and other items hoisted may fall from heights and damage vehicles.	Proper hoisting and lifting techniques will be used to ensure that materials do not fall from heights. F-Type concrete barriers will be installed such that loads are never suspended above the public realm.	Precast concrete panels and other items hoisted may fall from heights and injure pedestrians.	Proper hoisting and lifting techniques will be used to ensure that materials do not fall from heights. Pedestrians will be moved to opposite sides of street from the project site or onto temporary sidewalks such that loads are never suspended above the public realm.
9	Reinstatement of Public Infrastructure & Service Installation	Superstructure	Heavy equipment and hot concrete used during public infrastructure reinstatement and service installation may cause damage to vehicles.	The contractor shall maintain safe distances between vehicles and heavy machinery on-site. Concrete barriers will be installed to separate construction vehicles from public traffic during public infrastructure reinstatement and service installation.	Heavy equipment and hot concrete used during public infrastructure reinstatement may injure pedestrians.	The contractor shall maintain safe distances between pedestrians, vehicles, and heavy machinery.
10	Fallen debris	Superstructure	Debris may fall from upper stories of the new building causing damage to vehicles.	F-Type concrete barriers will be installed such that a safe distance is maintained between the building envelope and vehicular traffic.	Debris may fall from upper stories of the new building injuring pedestrians.	Construction of upper building levels will be set back from the property line/rigid fencing, this separating pedestrians from potential fallen debris.

Appendix L – Community Consultation Records

COMMUNITY CONSULTATION MAP OVERVIEW

Project – Portland & Carver Apartments



Notification Letter

Date: *****

Mayabella Homes – Building Construction Information Meeting

Dear Neighbour,

As you may be aware, we are planning an apartment building construction project located at 663 Portland Street in Dartmouth.

If you are interested in receiving more information about our construction plans, practices, schedule and to go over any questions you may have regarding construction of our new project please contact us to discuss. We would be happy to meet with you to discuss.


Thank you.

Johnny Anjoul

Cell: 902-209-6902

Email: johnnyanjoul@icloud.com

Appendix M – HRM Tree Detail

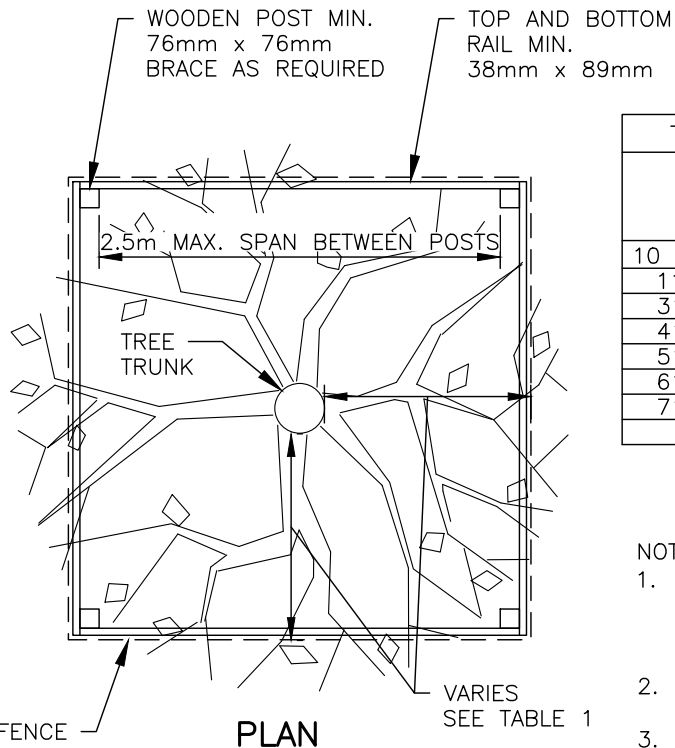


PLAN

TABLE 1

TREE PROTECTION ZONE CALCULATION TABLE	
TRUNK DIAMETER (DBH)	MINIMUM PROTECTION DISTANCE REQUIRED (MEASURE FROM THE OUTSIDE EDGE OF TREE TRUNK)
10 CM & UNDER	1.2 METERS
11 – 30 CM	2.0 METERS
31 – 40 CM	3.4 METERS
41 – 50 CM	4.6 METERS
51 – 60 CM	6.0 METERS
61 – 70 CM	7.0 METERS
71 – 80 CM	8.0 METERS
>80 CM	9.0 METERS

NOTES:

1. WOOD POST: (MIN. 76mm WIDTH) INSTALLED TO A DEPTH OF 500mm. TOP AND BOTTOM RAIL: (MIN. 38 x 89mm CONSTRUCTION, MAX. SPAN 2.5m), CROSS BRACING AS REQUIRED.
2. NO GROUND DISTURBANCE WITHIN 1.2 METER OF THE TREE TRUNK (I.E. POST INSTALLATION)
3. POSTS SET BACK FROM SIDEWALK AND CURB: MIN 300mm
4. FENCE MATERIAL: MINIMUM ORANGE BARRIER FENCE OR METAL CHAIN LINK FENCE
5. ATTACH A SIGN ON TWO SIDES OF THE TREE "PROTECTION ZONE DO NOT REMOVE FENCE DURING CONSTRUCTION"

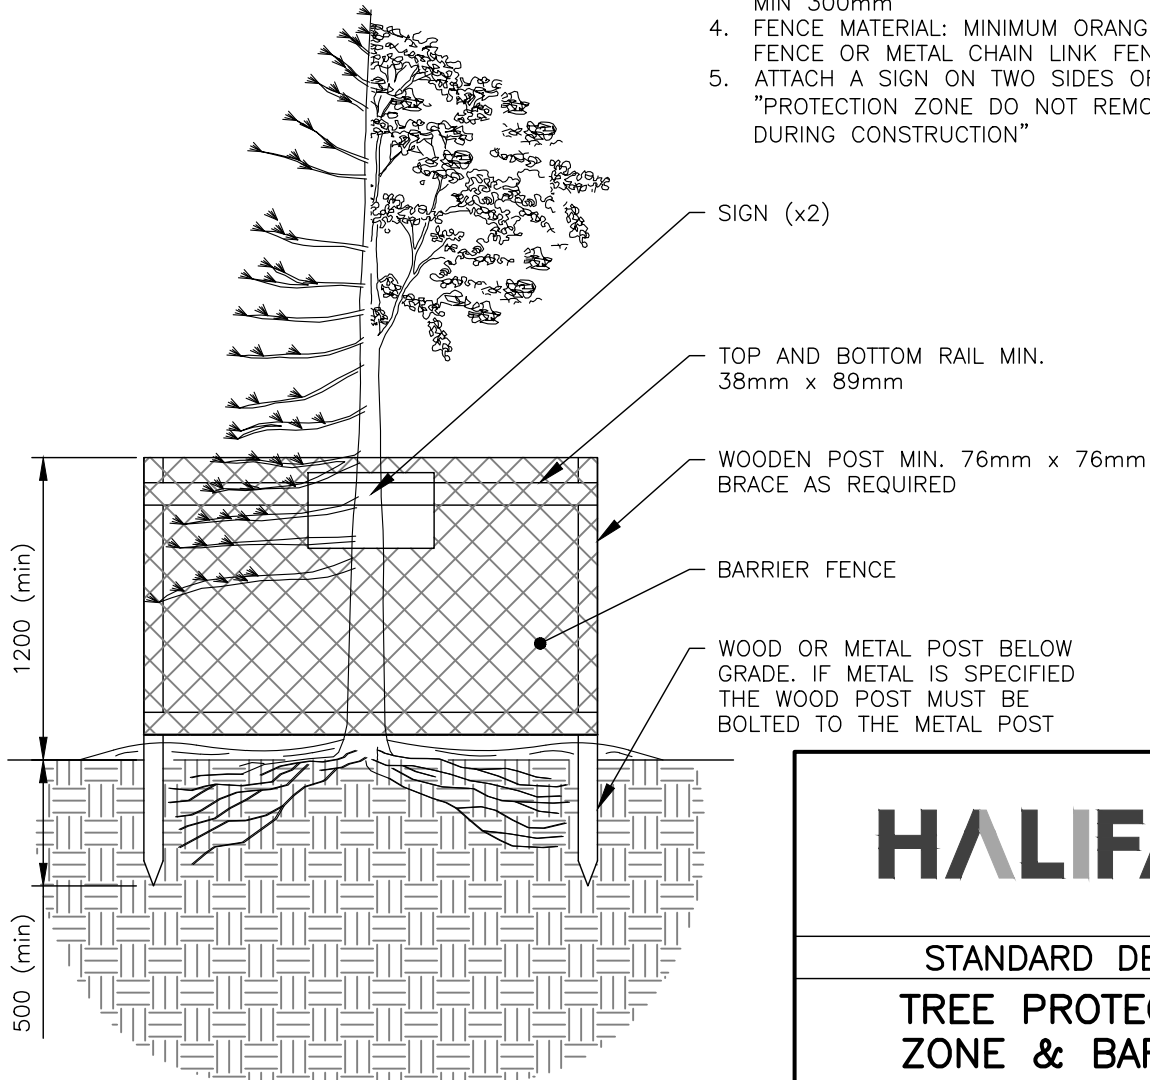

PROFILE


HALIFAX

STANDARD DETAIL

TREE PROTECTION ZONE & BARRIER

DATE:	REFERENCE	APPROVED
2021		
SCALE:		FIG No.:
NTS		HRM 140

Appendix N – Rodent Control Plan

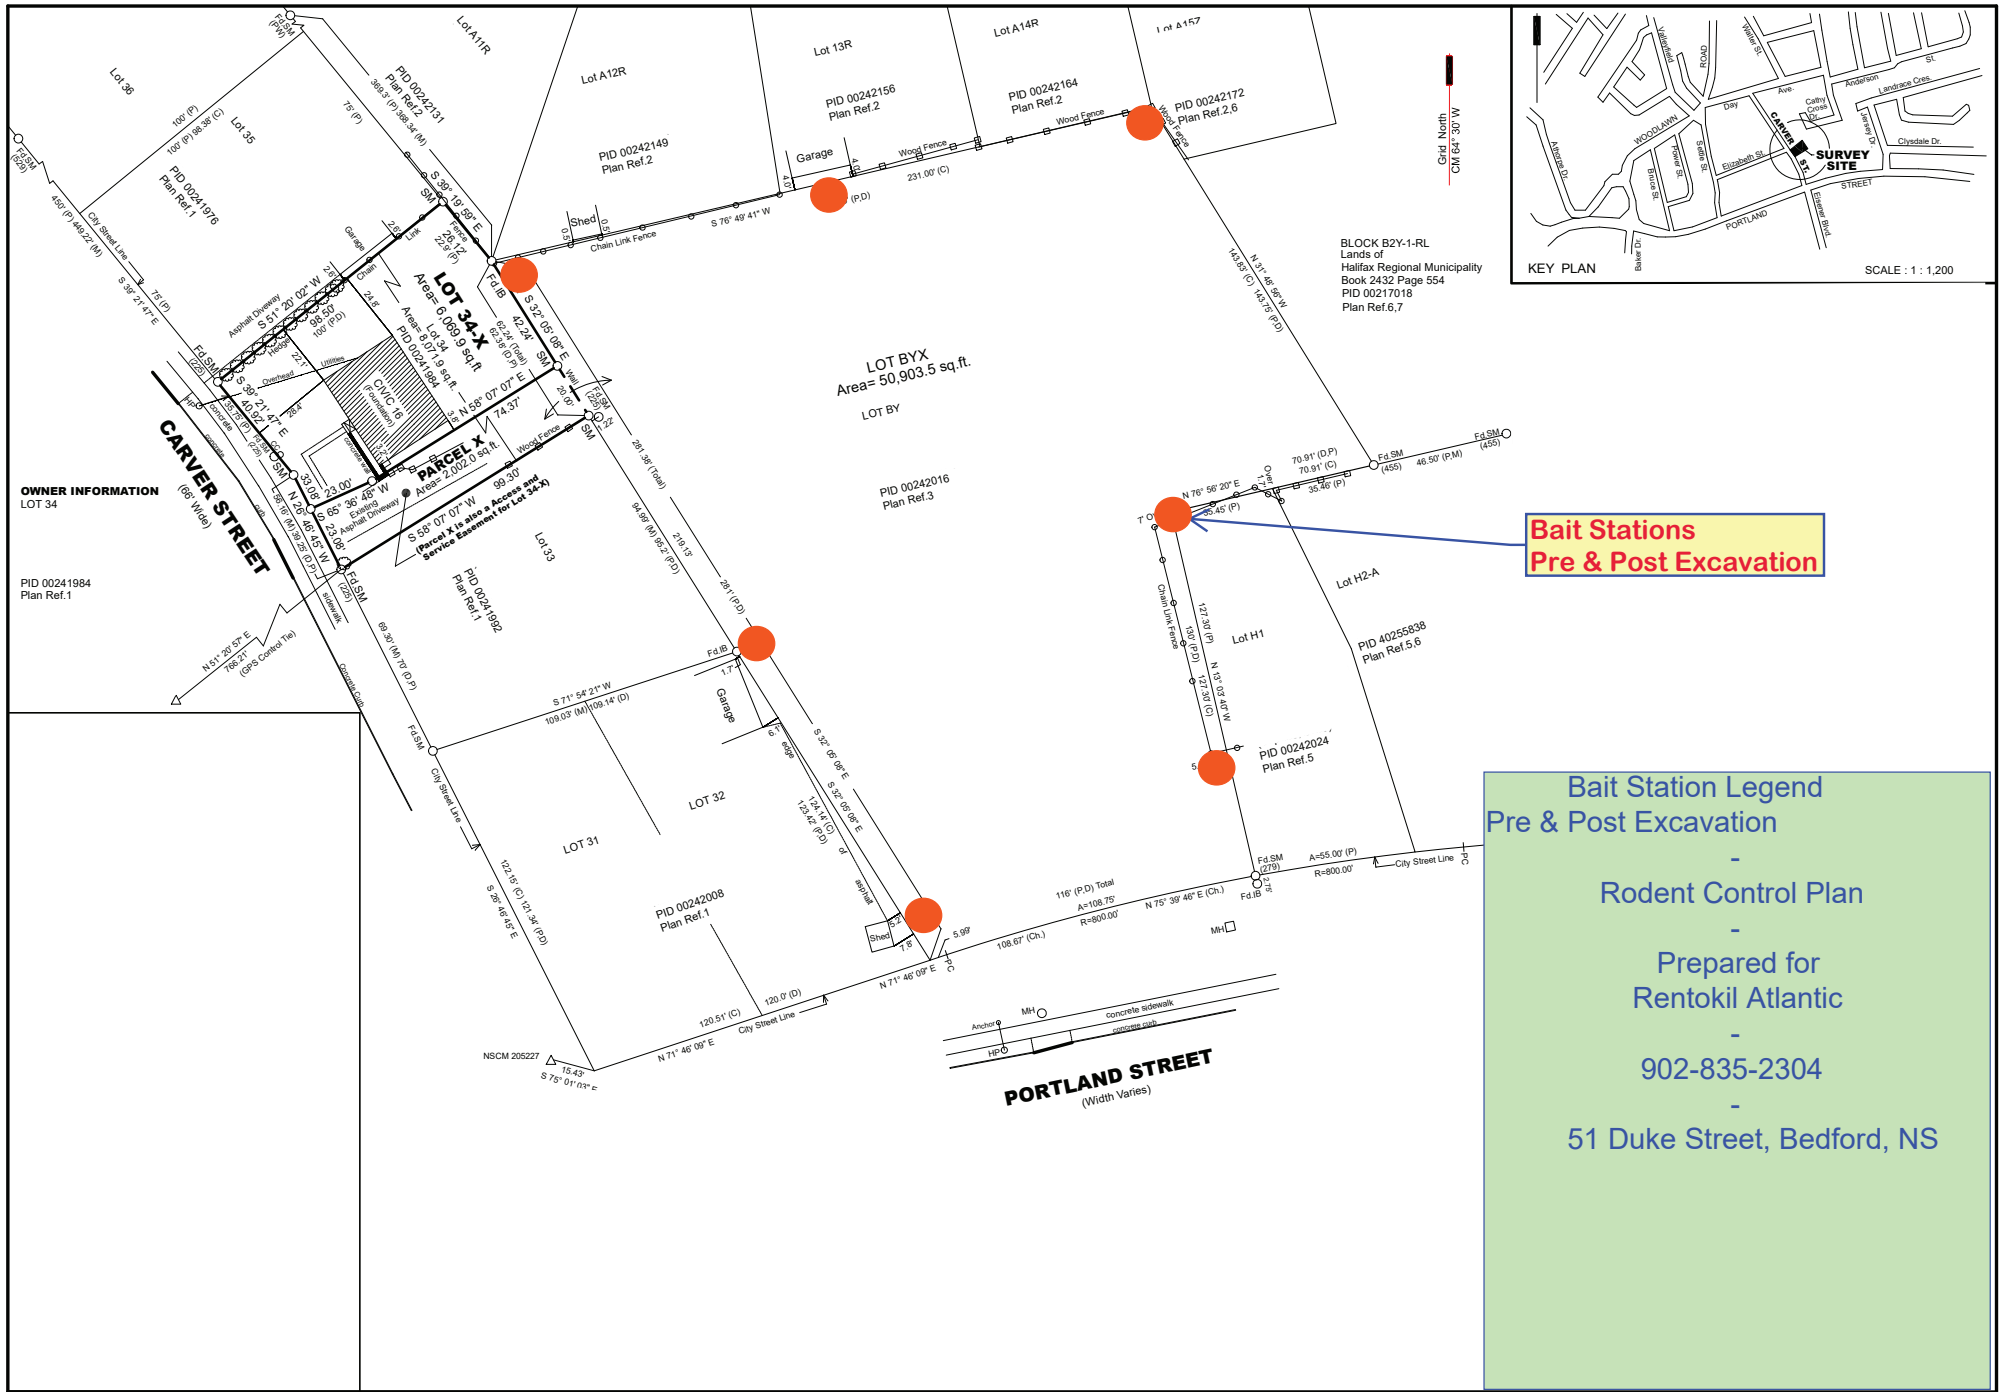


OWNER INFORMATION
LOT 34

PID 00241984
Plan Ref.1

BLOCK B2Y-1-RL
Lands of
Halifax Regional Municipality
Book 2432 Page 554
PID 00217018
Plan Ref.6,7

**Bait Stations
Pre & Post Excavation**

Bait Station Legend
Pre & Post Excavation
-
Rodent Control Plan
-
Prepared for
Rentokil Atlantic
-
902-835-2304
-
51 Duke Street, Bedford, NS

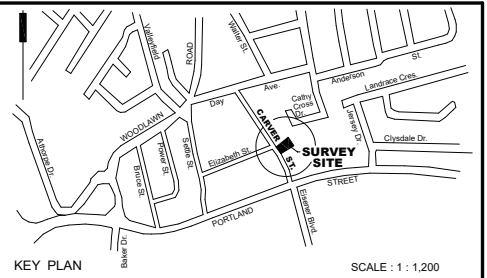

SCALE : 1 : 1,200

PORTLAND STREET
(Width Varies)

Grid North
GM 64 30' W

Protecta®
EVO® **AMBUSH™**
 PATENT PENDING



THE MOST ADVANCED LOW-PROFILE BAIT STATION

PRODUCT FEATURES:

- ▶ Single locking mechanism for quick servicing
- ▶ Removable tray for easy cleaning
- ▶ Locking bait rods won't fall out during cleaning
- ▶ Dog & child tamper-resistant
- ▶ Can hold:
 - 4 - 1 oz. bait BLOX on 4 vertical rods
 - or -
 - T-Rex™ rat trap or Mini-Rex™ mouse trap
- ▶ Compatible with Sidekick® Load-N-Lock™ system



PRODUCT	CODE	DIMENSIONS (in)	CASE QTY
Protecta Evo Ambush	EA2000	8 1/2 x 10 1/4 x 4 1/4	6 Stations



More Than Meets The Eye

Madison, Wisconsin 53704 USA | Ph: (608) 241-0202 | Fax: (608) 241-9631

www.belllabs.com

ALL-WEATHER
BLOX™



CONTRAC®
ALL-WEATHER BLOX™

KILLS RATS, MICE & MEADOW VOLES*

Kills Warfarin Resistant Norway Rats

KEEP OUT OF REACH OF CHILDREN

CAUTION

See back panels for First Aid and additional precautionary statements.

ACTIVE INGREDIENT:

Bromadiolone (CAS #28772-56-7): 0.005%

OTHER INGREDIENTS†: 99.995%

†Contains Denatonium Benzoate TOTAL 100.000%

*Not permitted for use against the following species in California: Cotton rat, Eastern harvest mouse, Golden mouse, Polynesian rat, Meadow vole, White-throated woodrat, Southern plains woodrat, and Mexican woodrat.

NET WT:
18 lbs (8.2 kg)

FIRST AID

HAVE LABEL WITH YOU WHEN OBTAINING TREATMENT ADVICE

IF SWALLOWED:

- Call a poison control center, doctor, or 1-877-854-2494, or 1-800-858-7378** immediately for treatment advice.
- Have person sip a glass of water if able to swallow.
- Do not induce vomiting unless told to do so by the poison control center or doctor.

IF ON SKIN OR CLOTHING:

- Take off contaminated clothing. Rinse skin immediately with plenty of water for 15–20 minutes.
- Call a poison control center or doctor for treatment advice.

IF IN EYES:

- Hold eye open and rinse slowly and gently with water for 15–20 minutes.
- Remove contact lenses, if present, after the first 5 minutes, then continue rinsing eye.
- Call a poison control center, doctor, or 1-877-854-2494 immediately for treatment advice.

** Also call this number for information on health concerns and pesticide incidents.

NOTE TO PHYSICIAN

If swallowed or absorbed through the skin, this material may reduce the clotting ability of the blood and cause bleeding. If ingested, administer Vitamin K₁ intramuscularly or orally. Repeat as necessary based on monitoring of prothrombin times.

TREATMENT FOR PET POISONING

If animal eats bait, call veterinarian at once.

NOTE TO VETERINARIAN

Anticoagulant Bromadiolone: For animals ingesting bait and/or showing poisoning signs (bleeding or elevated prothrombin times), give Vitamin K₁. If needed, check prothrombin times every 3 days until values return to normal (up to 30 days). In severe cases, blood transfusions may be needed.

DIRECTIONS FOR USE

It is a violation of Federal law to use this product in a manner inconsistent with its labeling.

READ THIS LABEL: Read this entire label and follow all use directions and use precautions. Use only for sites, pests, and application methods described on this label.

IMPORTANT: Do not expose children, pets, or nontarget animals to rodenticides. To help to prevent exposure:

1. Store unused product out of reach of children and pets.
2. Apply bait in locations out of reach of children, pets, domestic animals and nontarget wildlife, or in tamper-resistant bait stations. These stations must be resistant to destruction by dogs and by children under six years of age, and must be used in a manner that prevents such children from reaching into bait compartments and obtaining bait. If bait can be shaken from bait stations when they are lifted, units must be secured or otherwise immobilized. Stronger bait stations are needed in areas open to hoofed livestock, raccoons, bears, or other potentially destructive animals, or in areas prone to vandalism.
3. Dispose of product container and unused, spoiled, or unconsumed bait as specified on this label.

Bait stations are mandatory for outdoor, above-ground use. Tamper-resistant bait stations must be used wherever children, pets, non-target mammals, or birds may have access to the bait placement location.

USE RESTRICTIONS: This product may only be used to control the following rodent pests in and around man-made structures: House mouse (*Mus musculus*), Norway rat (*Rattus norvegicus*), Roof rat (*Rattus rattus*), Cotton mouse (*Peromyscus gossypinus*), Cotton rat* (*Sigmodon hispidus*), Deer mouse (*Peromyscus maniculatus*), Eastern harvest mouse* (*Reithrodontomys humuli*), Golden mouse* (*Ochrotomys nuttalli*), Polynesian rat* (*Rattus exulans*), Meadow vole* (*Microtus pennsylvanicus*), White-footed mouse (*Peromyscus leucopus*), White-throated woodrat* (*Neotoma albigula*), Southern plains woodrat* (*Neotoma micropus*), and Mexican woodrat* (*Neotoma mexicana*). This product must be used in and within 100 feet of man-made structures constructed in a manner so as to be vulnerable to commensal rodent invasions and/or to harboring or attracting rodent infestations. Examples of such structures include homes and other permanent or temporary residences, food processing facilities, industrial and commercial buildings, trash receptacles, agricultural and public buildings, transport vehicles (ships, trains, aircraft), docks and port or terminal buildings and related structures around and associated with these sites. Fence and perimeter baiting, beyond 100 feet from a structure as defined above, is prohibited. This product must not be applied directly to food or feed crops.

587CB-9

CONTRAC[®]

ALL-WEATHER BLOX[™]

KILLS RATS, MICE, AND MEADOW VOLES*

Kills Warfarin Resistant Norway Rats

Norway rats, roof rats, and house mice may consume a lethal dose in one night's feeding with first dead rodents appearing four or five days after feeding begins.

ACTIVE INGREDIENT:

Bromadiolone (CAS #28772-56-7): 0.005%

OTHER INGREDIENTS: 99.995%

†Contains Denatonium Benzoate TOTAL 100.000%

KEEP OUT OF REACH OF CHILDREN CAUTION

See side panels for First Aid and additional precautionary statements.

STORAGE AND DISPOSAL

Do not contaminate water, food or feed by storage or disposal.

Pesticide Storage: Store only in original container in a cool, dry place inaccessible to children and pets. Keep containers closed and away from other chemicals.

Pesticide Disposal: Wastes resulting from the use of this product may be placed in trash or delivered to an approved waste disposal facility.

Container Handling: Nonrefillable container. Do not reuse or refill this container. **[Plastic:]** Offer for recycling or reconditioning; or puncture and dispose of in a sanitary landfill; or by incineration. In most states, burning is not allowed.

WARRANTY: To the extent consistent with applicable law, seller makes no warranty, expressed or implied, concerning the use of this product other than indicated on the label. Buyer assumes all risk of use and/or handling of this material when such use and/or handling is contrary to label instructions.

NET WEIGHT: 18 lbs (8.2 kg)

EPA REG. NO. 12455-79

EPA EST. NO. 12455-WI-1

Manufactured by:

**Bell**
LABORATORIES, INC.
3699 Kinsman Blvd.
Madison, WI 53704 U.S.A.
www.bellabs.com
MADE IN USA

DIRECTIONS FOR USE (Continued from other panel)

Burrow baiting with Contrac All-Weather Blox is prohibited.

Do not place near or inside ventilation duct openings. Do not contaminate water, food, feedstuffs, food or feed handling equipment, or milk or meat handling equipment or surfaces that come into direct contact with food. When used in USDA inspected facilities, this product must be applied in tamper-resistant bait stations. Do not broadcast bait. Do not use this product in sewers.

Do not sell this product in individual containers holding less than 16 pounds of bait.

SELECTION OF TREATMENT AREAS: Determine areas where rats, mice, or meadow voles* will most likely find and consume the bait. Generally, these areas are along walls, by gnawed openings, in corners and concealed places, between floors and walls, or in locations where rats, mice, or meadow voles*, or their signs have been seen. Protect bait from rain and snow. Remove as much alternative food as possible.

APPLICATION DIRECTIONS:

RATS: Place 3 to 16 bait blocks (at intervals of 15 to 30 feet) per placement in infested areas. Maintain an uninterrupted supply of fresh bait for at least 10 days or until signs of rat activity cease.

MICE AND MEADOW VOLES*: Place 1 block per placement. Space placements at 8- to 12-foot intervals in infested areas. Two blocks may be needed at points of very high activity. Maintain an uninterrupted supply of fresh bait for at least 15 days or until signs of mouse or meadow vole* activity cease.

FOLLOW-UP: Replace contaminated or spoiled bait immediately.

Wearing gloves, collect and dispose of all dead, exposed animals and leftover bait. To prevent reinfestation, limit sources of rodent food, water, and harborage as much as possible. If reinfestation does occur, repeat treatment. Where a continuous source of infestation is present, establish permanent bait stations and replenish as needed.

PRECAUTIONARY STATEMENTS

HAZARDS TO HUMANS AND DOMESTIC ANIMALS

CAUTION: Harmful if swallowed or absorbed through the skin. Keep away from children, domestic animals and pets. Do not get in eyes, on skin or on clothing.

All handlers (including applicators) must wear: shoes plus socks, and waterproof gloves. Any person who retrieves carcasses or unused bait following application of this product must wear gloves.

User Safety Requirements

Follow manufacturer's instruction for cleaning/maintaining PPE. If no such instructions for washables, use detergent and hot water. Keep and wash PPE separately from other laundry. Remove PPE immediately after handling this product. Wash the outside of gloves before removing. As soon as possible, wash hands thoroughly after applying bait and before eating, drinking, chewing gum, using tobacco or using the toilet and change into clean clothing.

ENVIRONMENTAL HAZARDS

This product is extremely toxic to fish, birds and other wildlife. Dogs and predatory and scavenging mammals and birds might be poisoned if they feed upon animals that have eaten this bait. Do not apply this product directly to water or to areas where surface water is present or to intertidal areas below the mean high water mark. Runoff also may be hazardous to aquatic organisms in water adjacent to treated areas. Do not contaminate water when disposing of equipment wash water or rinsate.

*Not permitted for use against the following species in California: Cotton rat, Eastern harvest mouse, Golden mouse, Polynesian rat, Meadow vole, White-throated woodrat, Southern plains woodrat, and Mexican woodrat.

Product Code: CB4051

090415/09-15





DETEX[®] BLOX with LUMITRACK

SAFETY DATA SHEET

ACCORDING TO REGULATION: OSHA
Hazard Communication Standard 29 CFR 1910.1200

DATE OF ISSUE:
January 2016

PREPARED BY:
CAR

SECTION 1. PRODUCT AND COMPANY IDENTIFICATION

Product Identifier: DETEX[®] BLOX with LUMITRACK
EPA Registration Number: NA
Relevant identified uses of the substance or mixture and uses advised against
Relevant identified uses: Activity Monitoring - Ready to use
Uses advised against: Use only for the purpose described above

MANUFACTURER/SUPPLIER:

Bell Laboratories, Inc.
3699 Kinsman Blvd.
Madison, WI 53704, USA
Email: sds@belllabs.com
Phone: 608-241-0202
Medical or Vet Emergency: 877-854-2494 or 952-852-4636
Spill or Transportation Emergency: 800-424-9300 (CHEMTREC)

SECTION 2. HAZARDS IDENTIFICATION

Classification according to Regulation OSHA 1910.1200(d): Not classified
Signal Word: None
See Section 15 for information on FIFRA applicable safety, health, and environmental classifications.

SECTION 3. COMPOSITION/INFORMATION ON INGREDIENTS

Component	CAS No.	% By weight
Inert and Non-Hazardous Ingredients (Unlisted components are non-hazardous)	Proprietary	100.00%

SECTION 4. FIRST AID MEASURES

Description of first aid measures
Ingestion: Non-Toxic
Inhalation: Not applicable.
Eye contact: Non-Toxic
Skin contact: Non-Toxic
Most important symptoms and effects, both acute and delayed
Non-Toxic
Advice to physician: Non-Toxic
Advice to Veterinarian: Non-Toxic

SECTION 5. FIRE-FIGHTING MEASURES

Extinguishing media
Suitable Extinguishing Media: water, foam or inert gas.
Unsuitable Extinguishing Media: None known.
Special hazards arising from the mixture: High temperature decomposition or burning in air can result in the formation of toxic gases, which may include carbon monoxide.
Advice for firefighters: Wear protective clothing and self-contained breathing apparatus.

SECTION 6. ACCIDENTAL RELEASE MEASURES

Personal precautions, protective equipment and emergency procedures: None. Non-Toxic
Environmental precautions: None. Non-Toxic
Methods and materials for containment and cleaning up
For Containment: None. Non-Toxic
For Cleaning Up: None. Non-Toxic
Reference to other sections: Refer to Sections 7, 8 & 13 for further details of personal precautions, personal protective equipment and disposal considerations.

SECTION 7. HANDLING AND STORAGE

Precautions for safe handling: Do not use near heat sources, open flame, or hot surfaces. Non-Toxic.

Conditions for safe storage, including any incompatibilities: None. Non-Toxic

SECTION 8. EXPOSURE CONTROLS/PERSONAL PROTECTION

Established Limits

Component	OSHA	ACGIH	Other Limits
None	Not Established	Not Established	Not Established

Appropriate Engineering Controls: None. Non-Toxic

Occupational exposure limits: None. Non-Toxic

Personal Protective Equipment:

Respiratory protection: Not required

Eye protection: Not required

Skin protection: None. Non-Toxic

Hygiene recommendations: None. Non-Toxic

SECTION 9. PHYSICAL AND CHEMICAL PROPERTIES

Information on basic physical and chemical properties

Appearance/Color:	Tan wax block
Odor:	Sweet grain-like
Odor Threshold:	Not applicable, odor not associated with a hazardous material.
pH:	Not applicable, is not dispersible with water.
Melting point:	Not applicable
Boiling point:	Not applicable
Flash point:	Not applicable, does not contain components classified as flammable.
Evaporation rate:	Not applicable, is a solid.
Flammability:	Not applicable, is a solid.
Upper/lower flammability or explosive limits:	Not applicable, does not contain components classified as flammable or explosive.
Vapor Pressure:	Not applicable
Vapor Density:	Not applicable, is a solid
Relative Density:	1.13 g/mL @ 20°C
Solubility (water):	Not water soluble
Solubility (solvents):	Not applicable
Partition coefficient: n-octanol/water:	Not applicable
Auto-ignition temperature:	Not applicable, does not contain components classified as flammable.
Decomposition temperature:	Not applicable
Viscosity:	Not applicable, is not a liquid.

SECTION 10. STABILITY AND REACTIVITY

Reactivity: Not Applicable

Chemical stability: Not Applicable

Possibility of hazardous reactions: Refer to Hazardous decomposition products

Conditions to avoid: Avoid extreme temperatures (below 0°C or above 40°C).

Incompatible materials: Not Applicable

Hazardous decomposition products: Not Applicable

SECTION 11. TOXICOLOGICAL INFORMATION

Information on toxicological effects

Acute Toxicity

LD50, oral (ingestion): Not Toxic

LD50, dermal (skin contact): Not Toxic

LC50, inhalation: Not Toxic

Skin corrosion/irritation: Not Toxic

Serious eye damage/Irritation: Not Toxic.

Respiratory or skin sensitization: Not Toxic

Germ cell mutagenicity: Not Toxic

Carcinogenicity: Not Toxic

Components	NTP	IARC	OSHA
None	NA	NA	NA

Reproductive Toxicity: Not Toxic
Aspiration Hazard: Not Toxic
Target Organ Effects: Not Toxic

SECTION 12. ECOLOGICAL INFORMATION

Ecotoxicity Effects: Not Toxic
Persistence and degradability: Not Toxic
Bioaccumulative potential: Not Toxic
Mobility in Soil: Not Toxic.
Other adverse effects: None.

SECTION 13. DISPOSAL CONSIDERATIONS

Disposal: Wastes resulting from the use of this product may be placed in trash, on-site, or at an approved waste disposal facility. Dispose of all wastes in accordance with all Federal, state and local regulations.

SECTION 14. TRANSPORT INFORMATION

UN number: Not regulated
UN proper shipping name: Not regulated
Transport hazard class(es): Not regulated
Packing group : Not regulated
Environmental Hazards
DOT Road/Rail: Not considered hazardous for transportation via road/rail.
DOT Maritime: Not considered hazardous for transportation by vessel.
DOT Air: Not considered hazardous for transportation by air.
Freight Classification: LTL Class 60
Transport in bulk according to Annex II of MARPOL 73/78 and the IBC code: Not applicable
Special precautions for user: None

SECTION 15. REGULATORY INFORMATION

Safety, health and environmental regulations/legislation specific for the substance or mixture: Not applicable
Signal Word: None
Precautionary Statements: None
Potential Health Effects:
Eye Contact: May cause irritation
Skin Contact: Non-irritating to the skin
Ingestion: Not harmful if swallowed

TSCA: All components are listed on the TSCA Inventory or are not subject to TSCA requirements
CERCLA/SARA 313: Not Toxic
CERCLA/SARA 302: Not Toxic

SECTION 16. OTHER INFORMATION


For additional information, please contact the manufacturer noted in Section 1.

NFPA	Health: 0 (Not Toxic)	Flammability: 1 (slight)	Reactivity: 0 (stable)	Specific Hazard: None
HMIS	Health: 0 (Not Toxic)	Flammability: 1 (slight)	Reactivity: 0 (minimal)	Protective Equipment: None



Disclaimer: The information provided in this Safety Data Sheet has been obtained from sources believed to be reliable. Bell Laboratories, Inc. provides no warranties; either expressed or implied, and assumes no responsibility for the accuracy or completeness of the data contained herein. This information is offered for your consideration and investigation. The user is responsible to ensure that they have all current data, including the approved product label, relevant to their particular use.

Appendix O – CMP’s TCP & PMP Inspection Records

Appendix P – Concrete Delivery Schematic

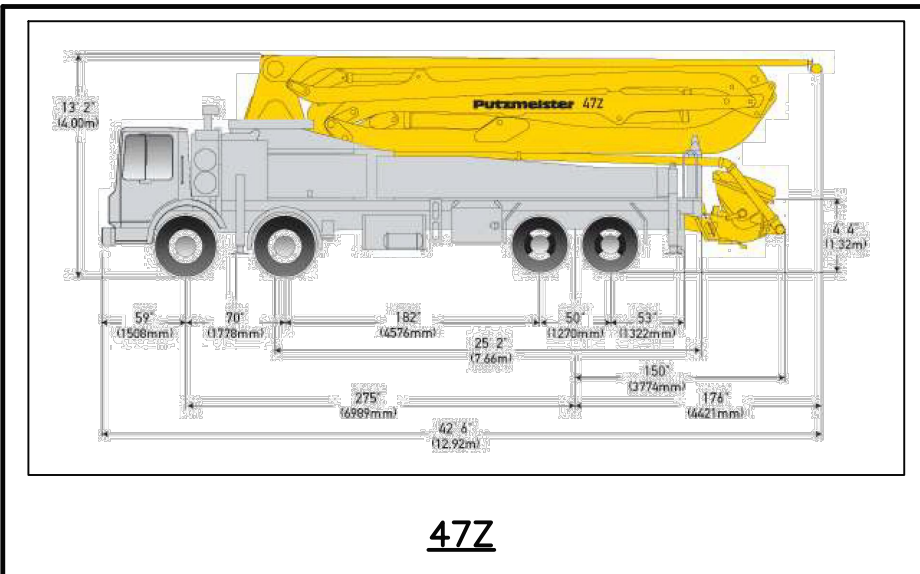

47Z

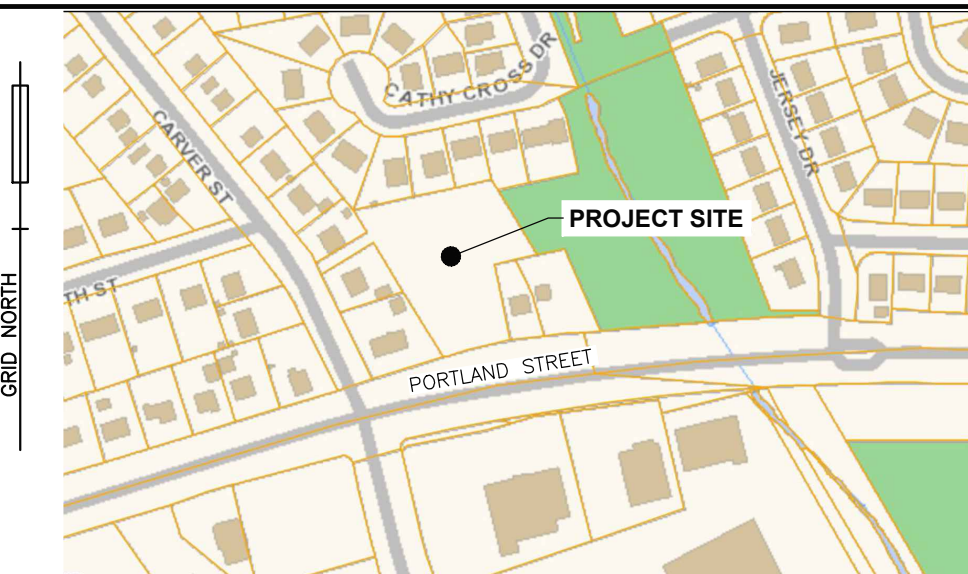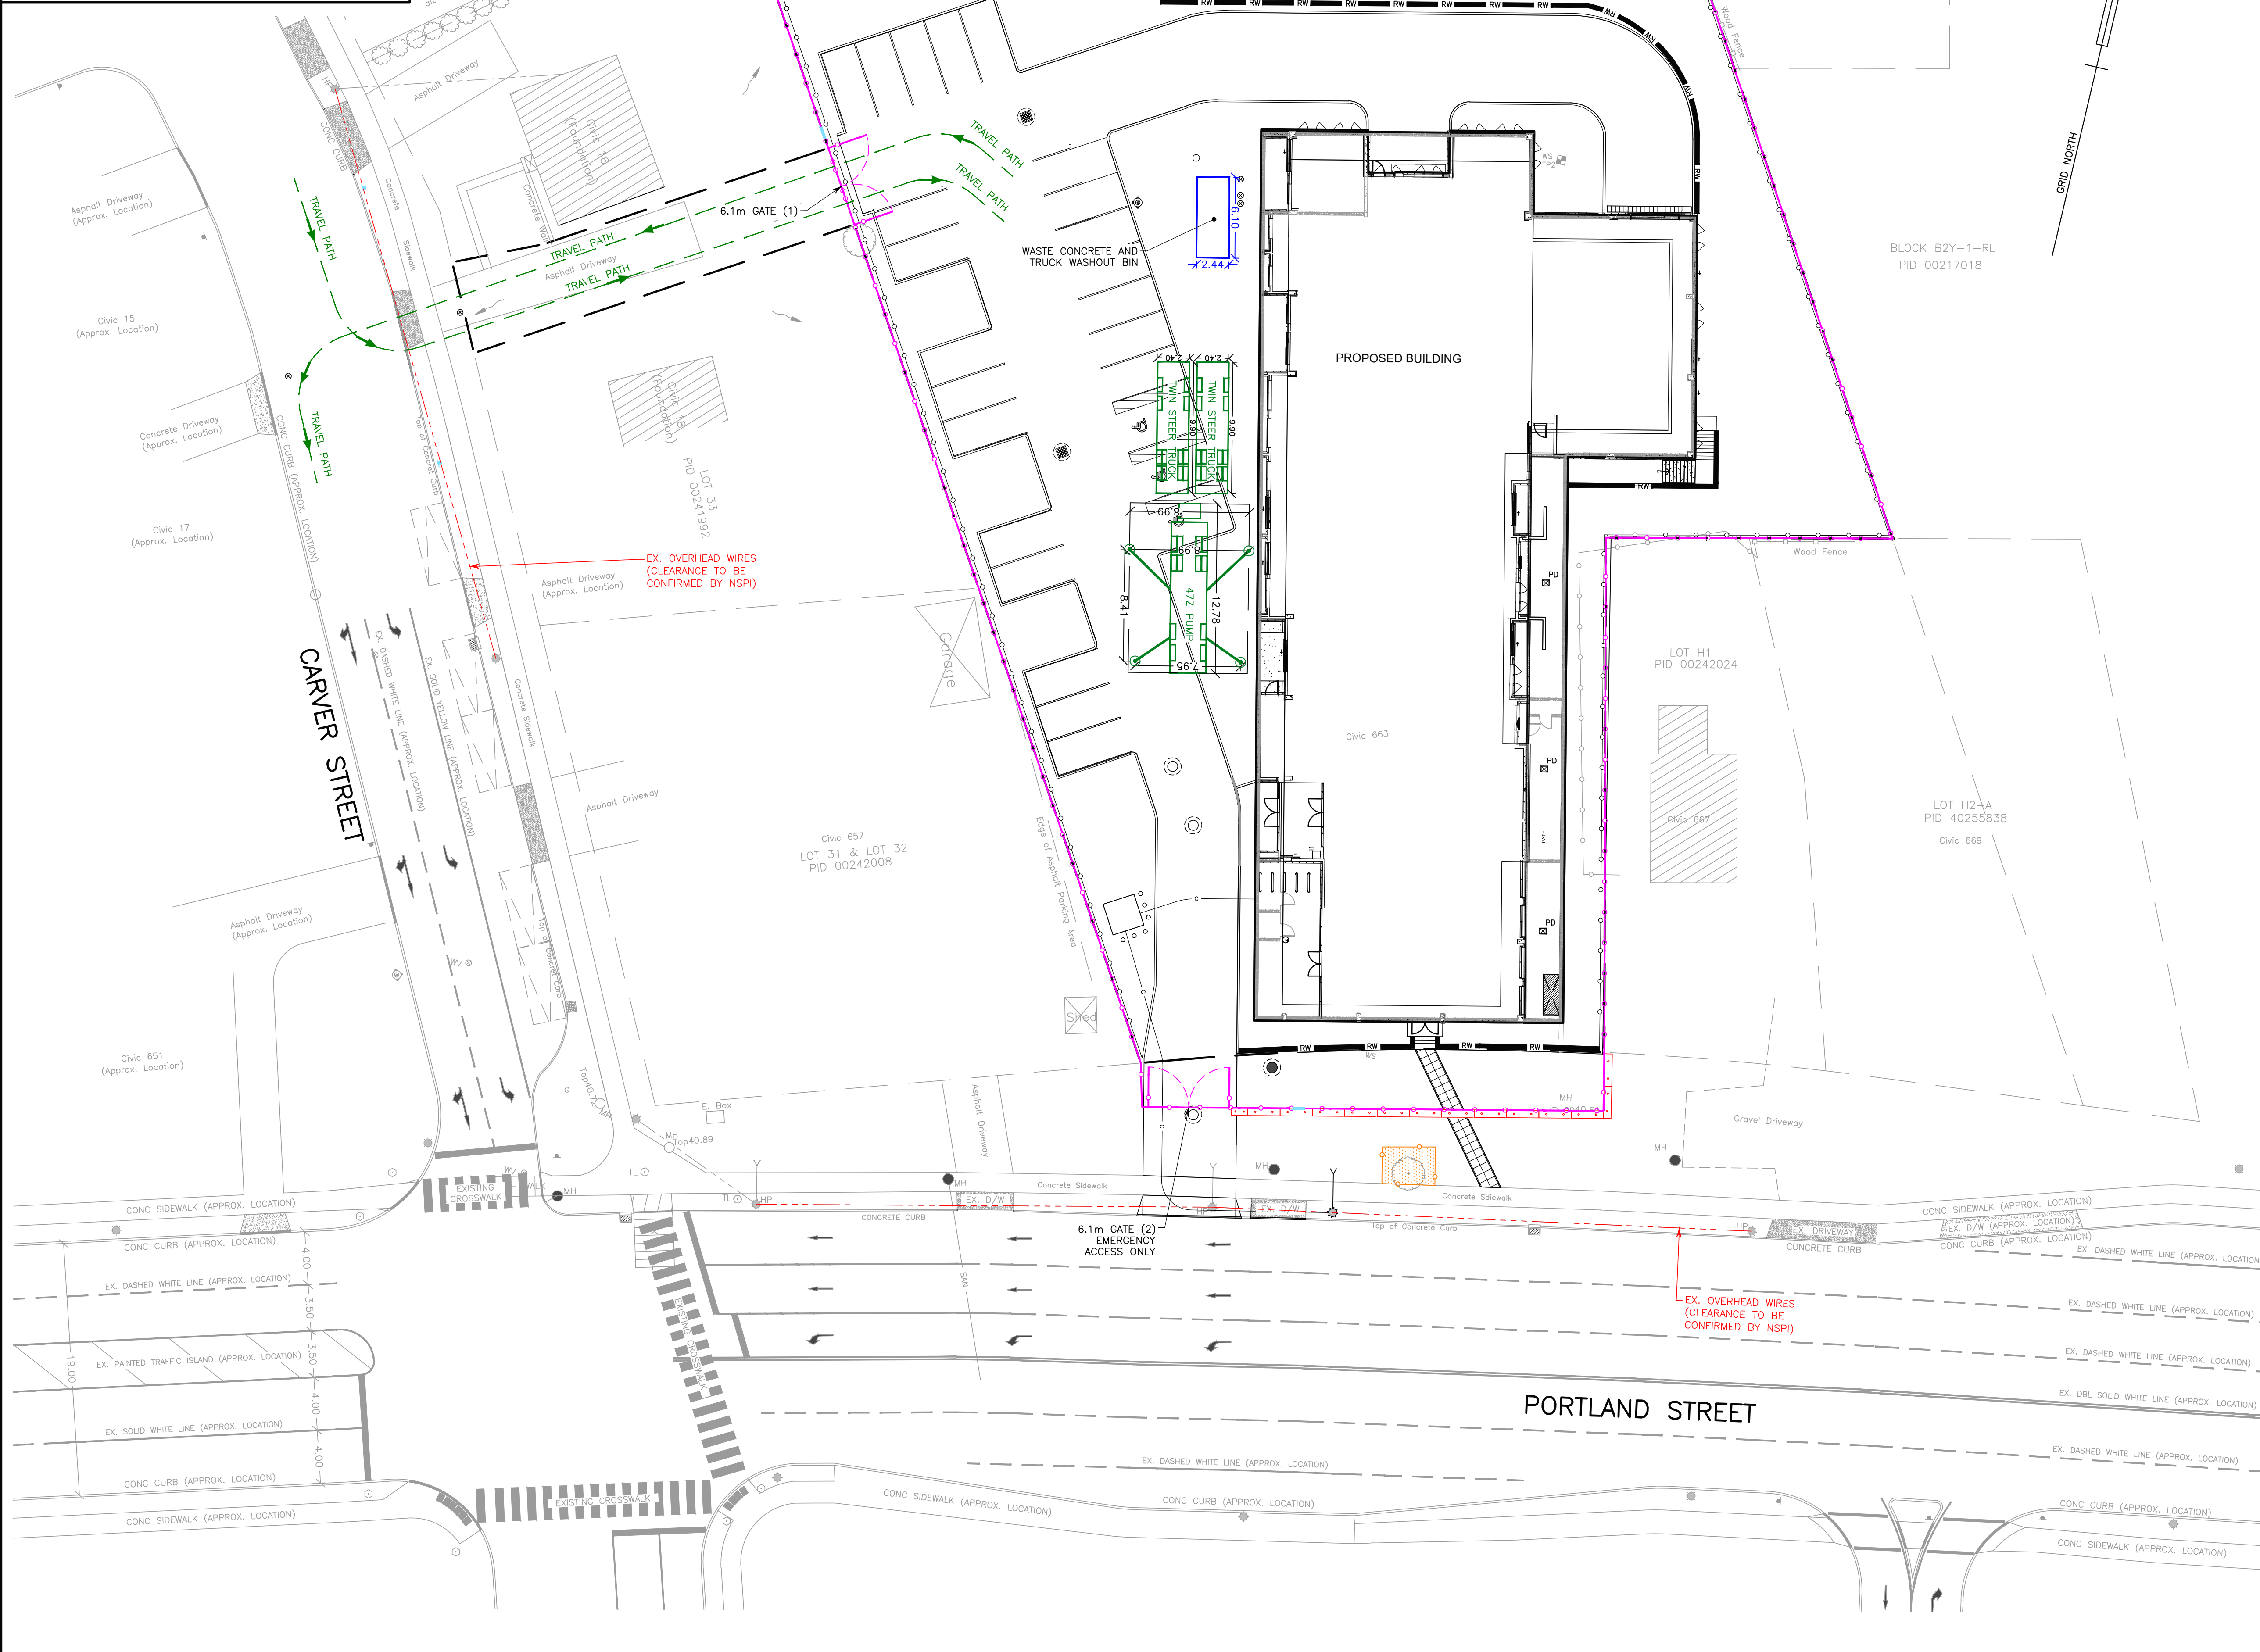

KEY PLAN



LEGEND

EXISTING	PROPOSED
25.0	25.0
CONTOUR LINE	CONTOUR LINE
○/○BF	○/○BF
CURB STOP/GATE/BUTTERFLY VALVE	CURB STOP/GATE/BUTTERFLY VALVE
○	○
FIRE HYDRANT	FIRE HYDRANT
□	□
CONCRETE THRUST BLOCK	CONCRETE THRUST BLOCK
○	○
SIAMSESE CONNECTION	SIAMSESE CONNECTION
□	□
CATCH BASIN/PIT	CATCH BASIN/PIT
○	○
CULVERT	CULVERT
○/○	○/○
ROCK LINING/DAM	ROCK LINING/DAM
○/○	○/○
ROCK WALL/RETAINING WALL	ROCK WALL/RETAINING WALL
○/○	○/○
POWER POLE & ANCHOR/LIGHT STANDARD	POWER POLE & ANCHOR/LIGHT STANDARD
○	○
TREE	TREE
○	○
STREET SIGN/PARKING METER	STREET SIGN/PARKING METER
○	○
ELEVATION/GRADE	ELEVATION/GRADE
x 131.82	125.00 x / 125.00
TEST PIT	TEST PIT
○	○
DRAINAGE/SWALE FLOW DIRECTION	DRAINAGE/SWALE FLOW DIRECTION
→	→
W	W
WATER MAIN/SERVICE	WATER MAIN/SERVICE
○	○
SAN	SAN
SANITARY MANHOLE & PIPE	SANITARY MANHOLE & PIPE
○	○
STM	STM
STORM MANHOLE & PIPE	STORM MANHOLE & PIPE
○	○
SAV/STM	SAV/STM
COMBINED PIPE	COMBINED PIPE
○	○
GAS	GAS
GAS LINE	GAS LINE
○	○
FL	FL
100YR. FLOOD LIMIT	100YR. FLOOD LIMIT
○	○
GUARD RAIL	GUARD RAIL
○	○
UNDERGROUND CONDUIT	UNDERGROUND CONDUIT
○	○
OVERHEAD WIRES	OVERHEAD WIRES
○	○
PROPERTY LINE/BOUNDARY	PROPERTY LINE/BOUNDARY
○	○
FENCE	FENCE
○	○
BUILDING	BUILDING
○	○
TOP OF SLOPE	TOP OF SLOPE
○	○
TOE OF SLOPE	TOE OF SLOPE
○	○
TREELINE	TREELINE
○	○
LIMITS OF DISTURBANCE	LIMITS OF DISTURBANCE
○	○
TACTILE PEDESTRIAN PLATES	TACTILE PEDESTRIAN PLATES
○	○
PROJECT SAFETY SIGNAGE	PROJECT SAFETY SIGNAGE
○	○
ORANGE SANHORSE BARRICADE	ORANGE SANHORSE BARRICADE
○	○

NOTES

1. THIS PLAN IS IN METRIC.
2. EXISTING CONDITIONS WITH APPROXIMATE LOCATIONS ARE BASED ON GOOGLE AERIAL IMAGERY AS SITE HAS NOT BEEN FIELD SURVEYED; DIMENSIONS MAY VARY AND SHALL BE CONFIRMED BY CONTRACTOR BEFORE PROCEEDING WITH CONSTRUCTION.

No.	YY/MM/DD	Revision	Description	Appr'd
1	24/07/25		REVISED AS PER CLIENT COMMENTS	
0	24/06/26		ISSUED FOR PERMIT	



PROPOSED APARTMENT BUILDING
663 PORTLAND STREET
DARTMOUTH, NOVA SCOTIA

CONCRETE DELIVERY SCHEMATIC		
Date	Drawn	Project No.
JUNE 26, 2024	D. ANDERSON	FILE NO. 1-7-135 (38410)
Scale	Engineer	Plan No.
1:250	G. MACLEAN	
Reference	Approved	Drawing Name
--	G. MACLEAN	R2
Surveyed	Sheet	
BY OTHERS		

